

MSC Project Update

Stakeholder Meeting
September 19, 2019


MSC - Project Components

MSC Project

1. MSC Concourse - 15 Gates
2. Gateway
3. PAX Tunnel
4. Utilidor / Crossover Tunnel
5. Taxilanes & Apron
6. DWP Substation


Baggage Optimization Project (BOP)


1. Far East Tunnel
2. North BHS Structure
3. North Tunnel

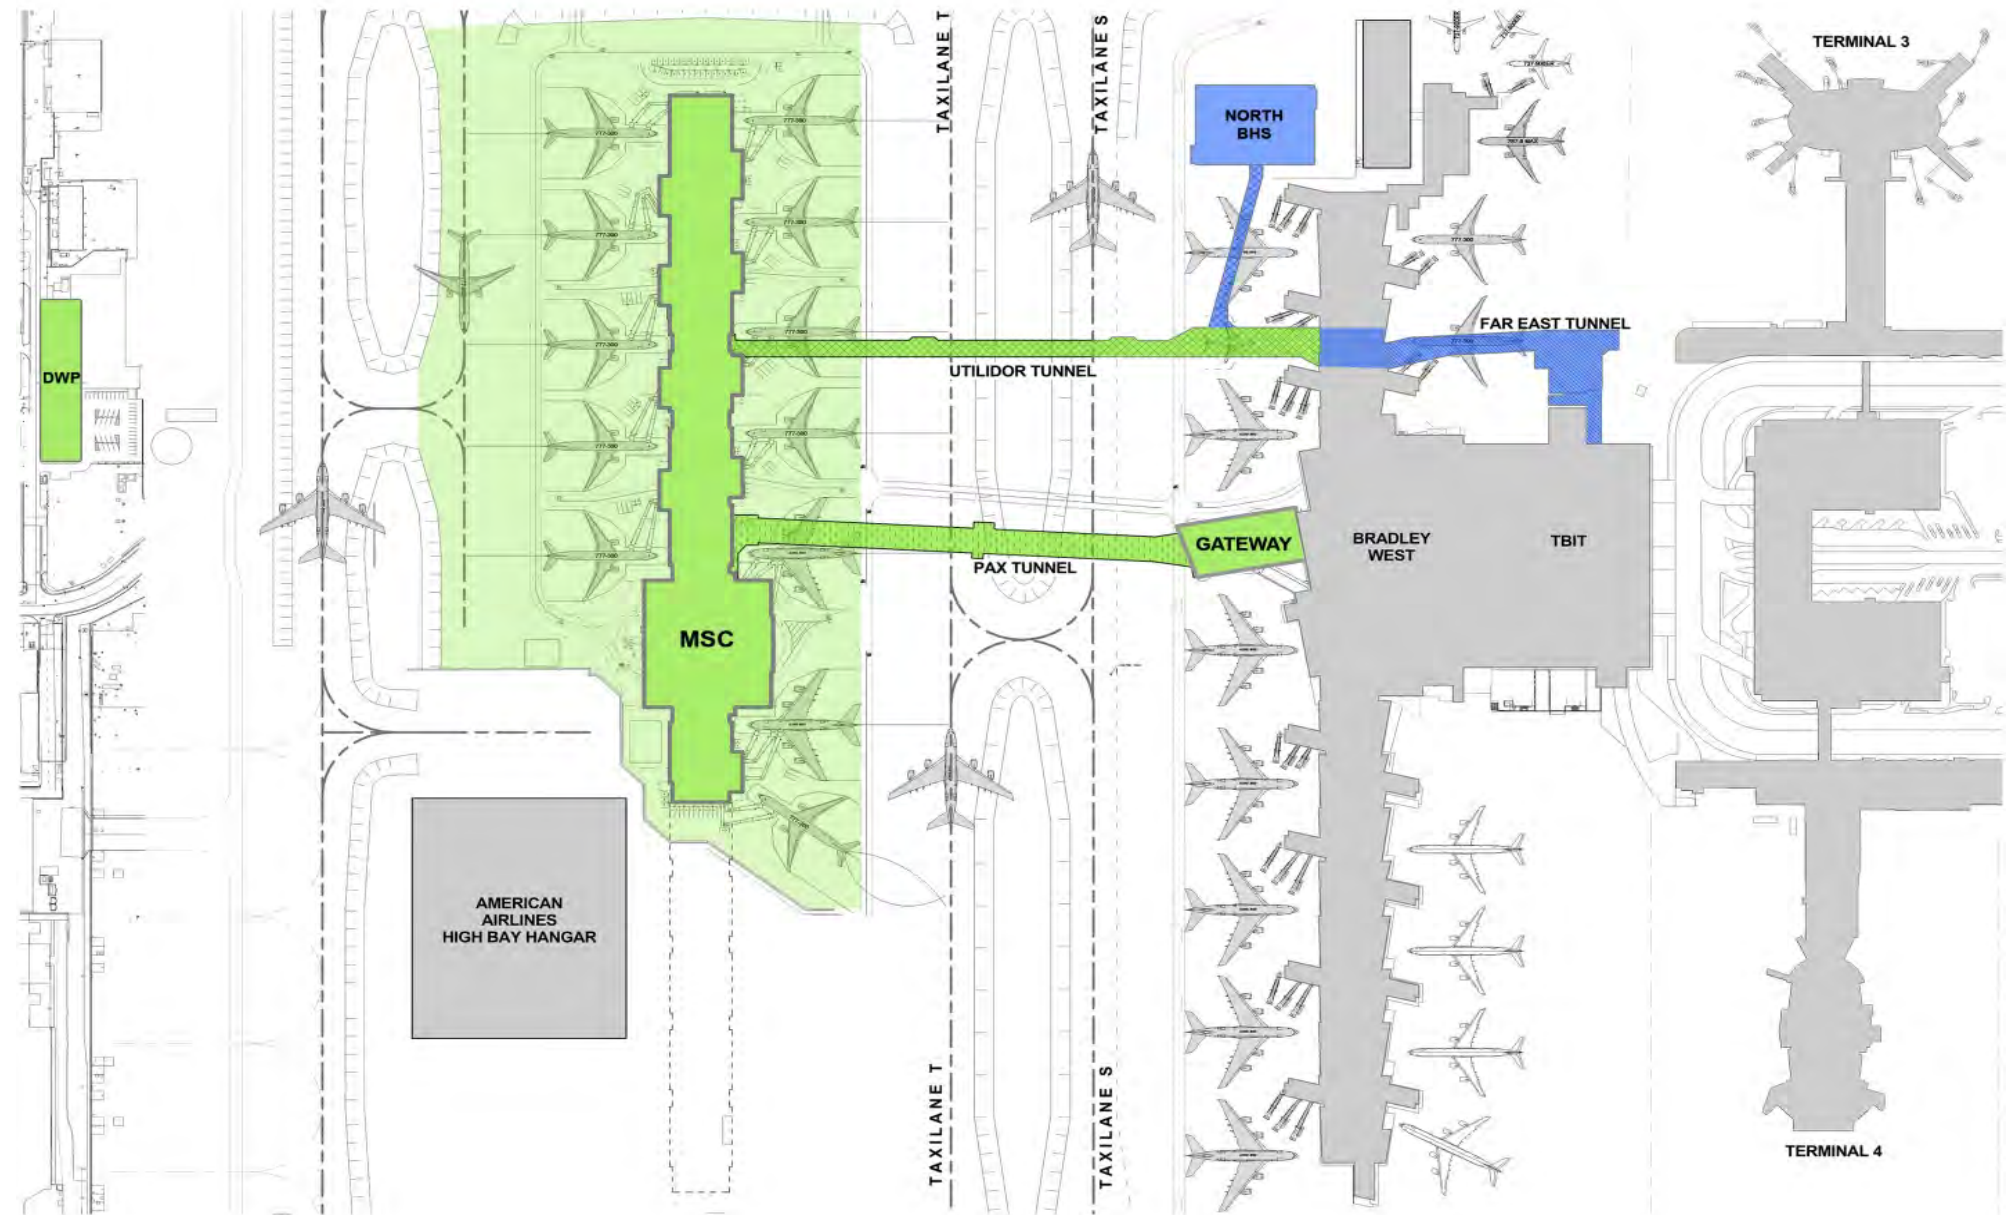

Updates by Geography

- ☐ MSC
 - ☐ Concourse
 - ☐ Civil
- ☐ Tunnels
 - ☐ TPAX
 - ☐ Utilidor
- ☐ Gateway
- ☐ BOP
 - ☐ BOP NBHS (IWBT)
 - ☐ BOP Far East Tunnel (Gate 131)
- ☐ BHS

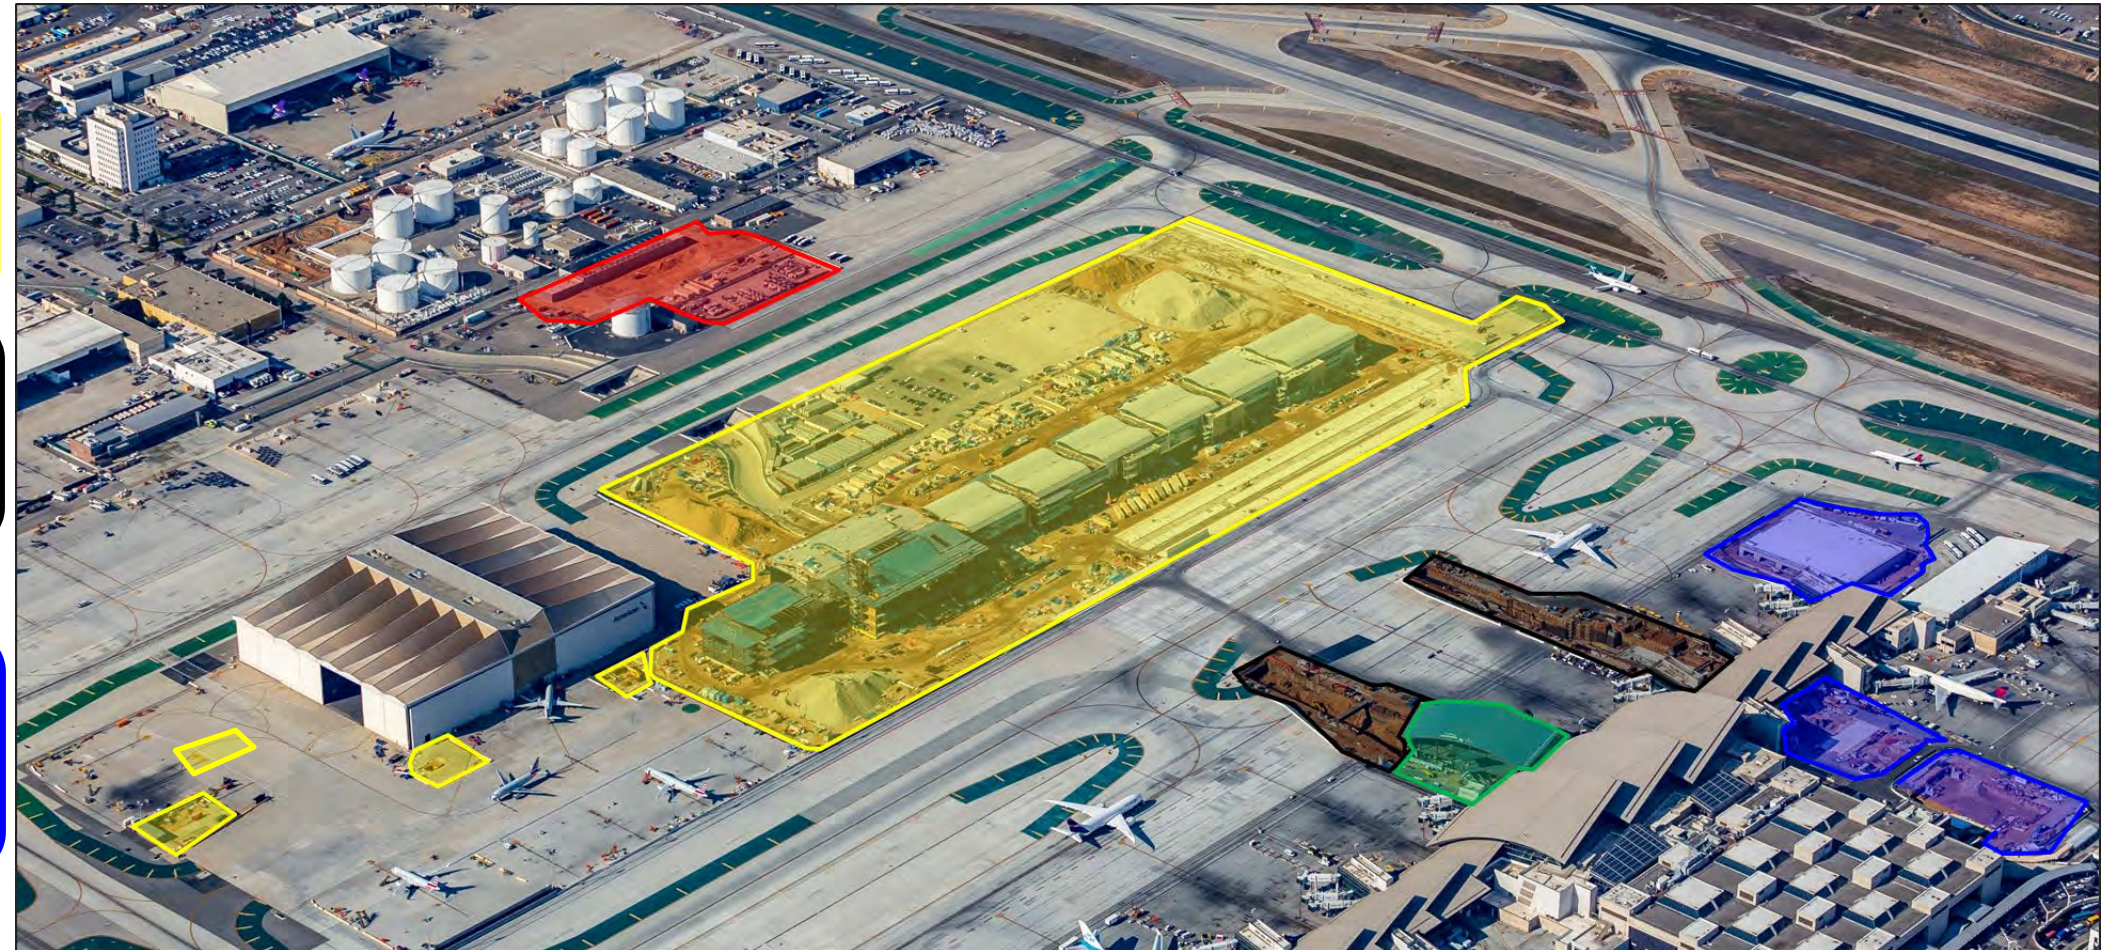

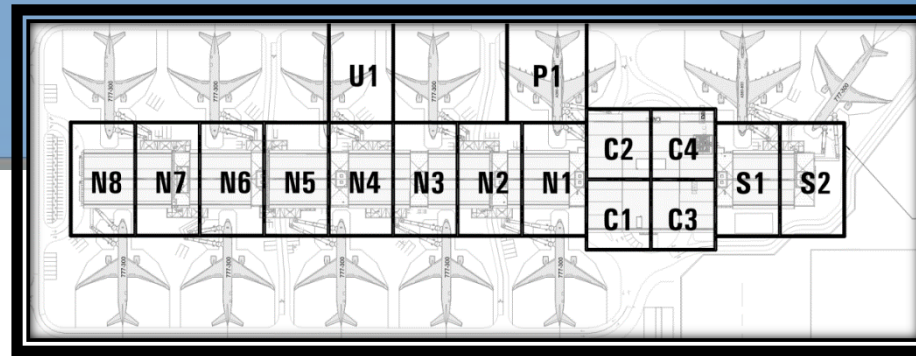

General Updates / Progress:



- ☐ Metal roofing installation at S1 & S2, Core
- ☐ Sidewalks / curb concrete pours at N3-N1 areas, N8-N4 mostly complete
- ☐ Terrazzo progressing south, complete with C1-C3 end of this week
- ☐ Building enclosure buttoning up at Core, S2, S1
- ☐ Westfield concession spaces being framing out moving towards N5
- ☐ Mechanical system blowing cold air 24hrs day at AHU 301 & 302, AHU 101 & 102 this week
- ☐ Site paving progressing at east/west apron N1 thru N8



Upcoming / Ongoing Coordination:

- ☐ Group III construction coordination ongoing
- ☐ DAS upgrades progressing and being coordinated with TPJV weekly
- ☐ Ongoing coordination walk with TPJV/LAWA Maintenance for MEP access
- ☐ Ongoing coordination/punch-walk with TPJV/ Design Team/IMTG to hand over (8) IT Rooms to LAWA to start network switches



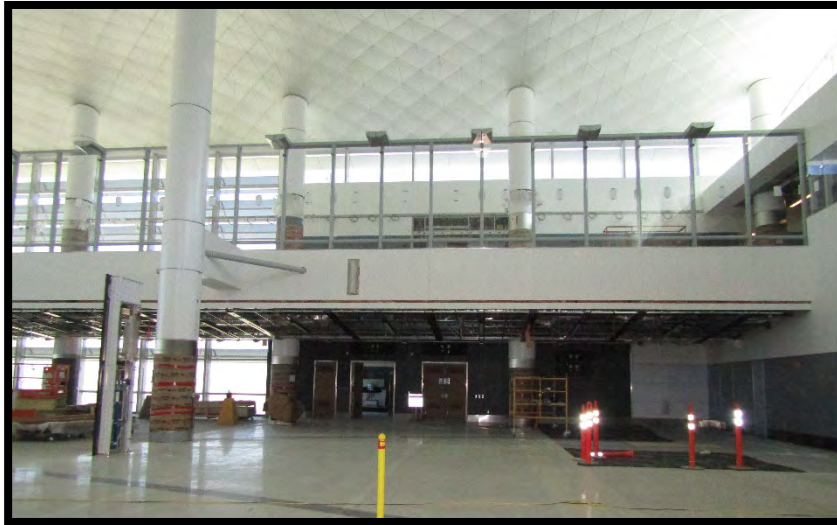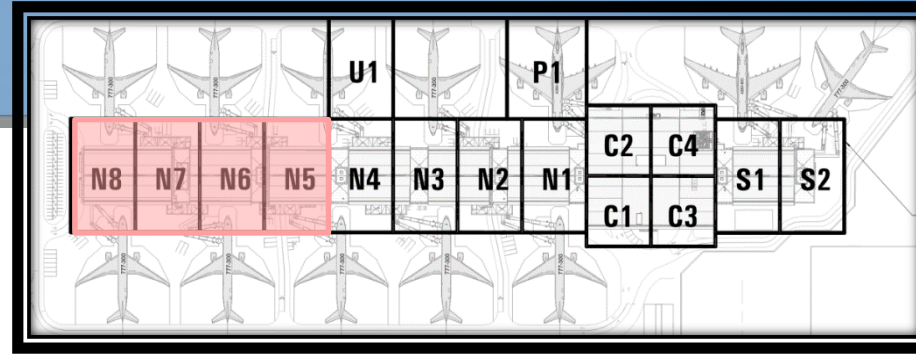

Finishes around Gatehouse 209
-various architectural finishes starting to come together (column covers, glass wall, carpet, base, Terrazzo etc.)



Neutral Framing at Concession Spaces N8
-finishes wrapping steel, security screen, and framing out at the concession spaces
-most of MEP access has been coordinated at these spaces



West Elevation N5 thru N8
-metal panel, roofing, and curtain wall about 99% complete
-aircraft paving in progress about 65% complete



Completed Terrazzo at Concourse N5
-last section to complete between before barrier to N1-N4




G210 Finishes
-phenolic panels, base, wire ceiling, security devices, door Hardware



1

West Elevations of Enclosures / Site work


- curtain wall, roof, exterior panels about 95% complete
- Runway pavement / sidewalks / curbs also in progress

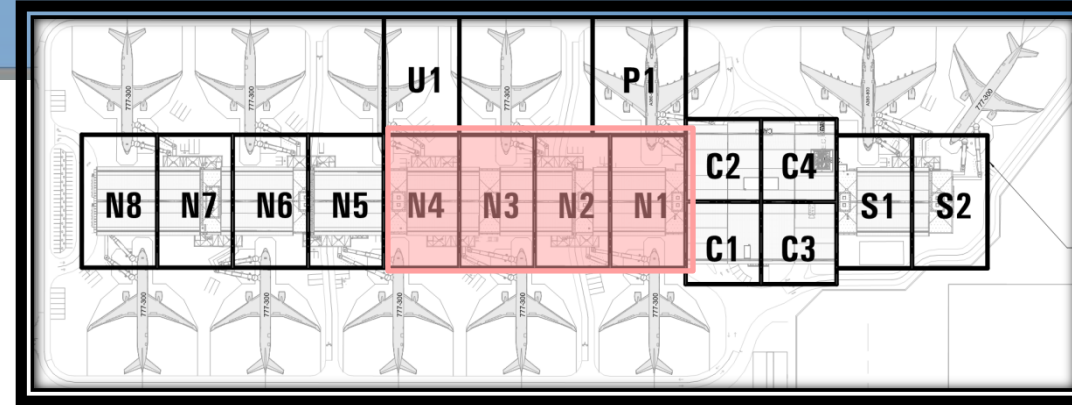

4

Baggage Carousels Conveyors at Apron N4

- this one of the northern carousels as VDI progresses north

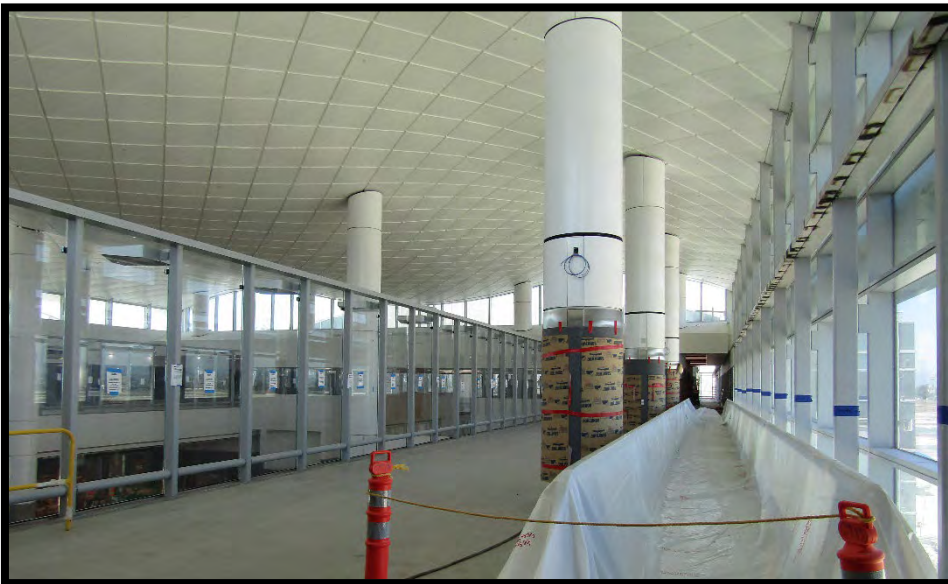

2

Sterile Level West Corridor N4

- various finishes in place (ceilings, glass wall, column covers)



3

N2 West Elevation Metal Panel

- last section of exterior metal panel to complete at N1 through N4




5

Neutral Framing at Concession Spaces N5


- Finish material wrapping steel at concession spaces
- ongoing coordination for utility access within these spaces



1

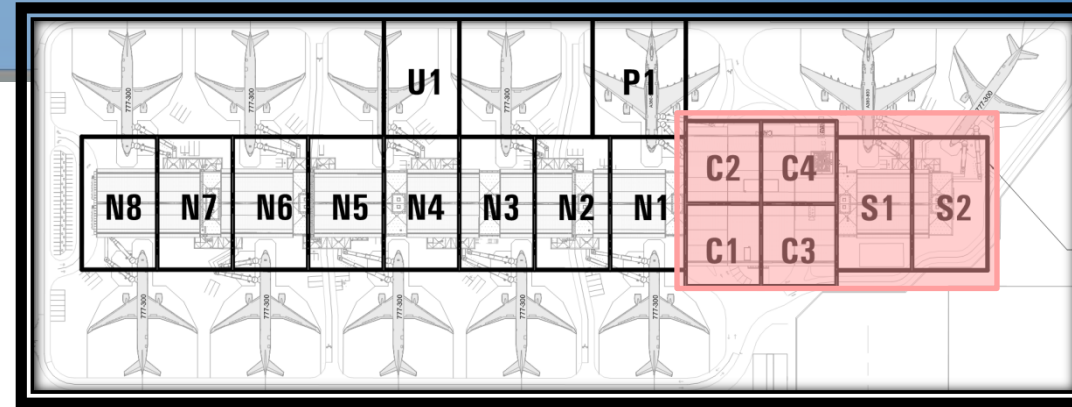


3

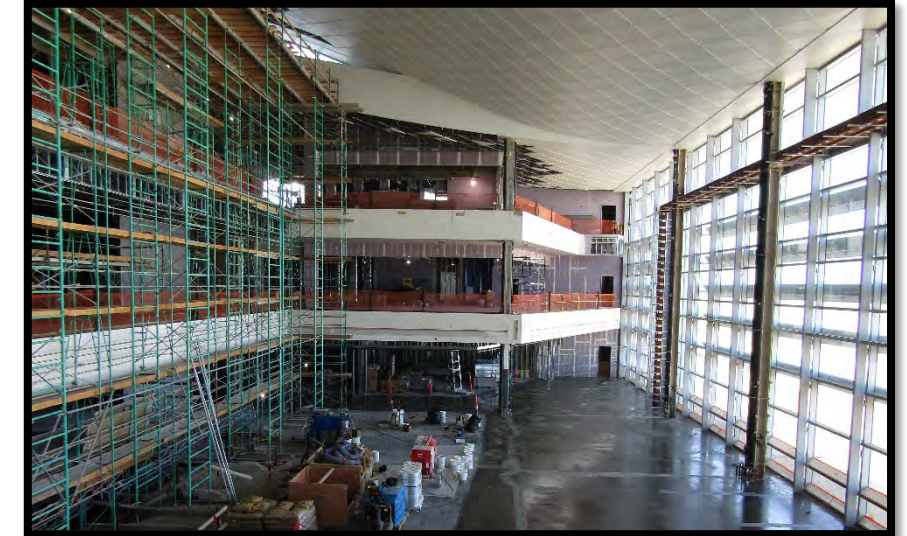

4

Core East Side Interiors (Picture Frame)

-Scaffolding has been removed with ceiling complete, now Terrazzo is in progress.

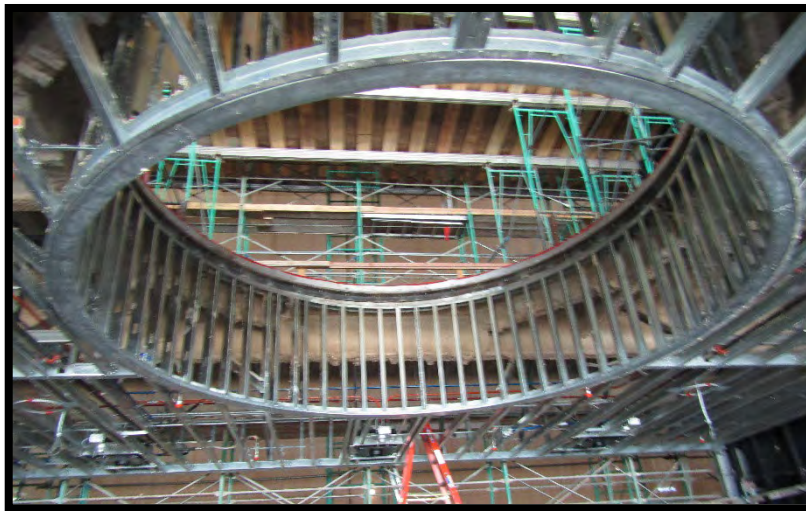

2

Center Artwork Display

-framing and sheathing the open ceiling for chandelier artwork display.

Core West Side Interiors (Picture Frame)

-Scaffolding has been removed with ceiling complete working on various finishes: Terrazzo, framing, sheathing, etc.



5

Apron Bus Pass

-Concrete topcoat complete, various MEP work in progress above ceiling

General Updates / Progress:

- ❑ Milestones are furniture Notice to Fabricate and Equipment order

Upcoming Coordination:

- ❑ Ongoing communication with Airport Ops and FAA



Ramp Control Tower View - Looking North

MSC Ramp Control Tower



Left: Hatch and stairs

Top: Looking north

MSC Civil – South Fence Relocation

General Updates:

- ☐ Fence relocation removes RON E6
- ☐ Fence relocation complete
- ☐ Cutover for RONs 9/2019

Upcoming Coordination:

- ☐ AA as needed



Updates by Geography

- ☐ MSC
 - ☐ Concourse
 - ☐ Civil
 - ☐ Tunnels
 - ☐ TPAX
 - ☐ Utilidor
- ☐ Gateway
- ☐ BOP
 - ☐ BOP NBHS (IWBT)
 - ☐ BOP Far East Tunnel (Gate 131)
- ☐ BHS




General Updates:

- ☐ Waterproofing continues at exterior
- ☐ Backfill continues over tunnel
- ☐ Framing continues inside tunnel
- ☐ Overhead MEPs continue in tunnel
- ☐ Underground Utilities over tunnel
- ☐ Jet Fuel IVP at South VSR
 - ☐ Operation ongoing

Upcoming Coordination:

- ☐ Temporary VSR Phasing Plan
 - ☐ Asphalt Paving 9/21 ~12hrs
 - ☐ Planned Activation : 9/26/19

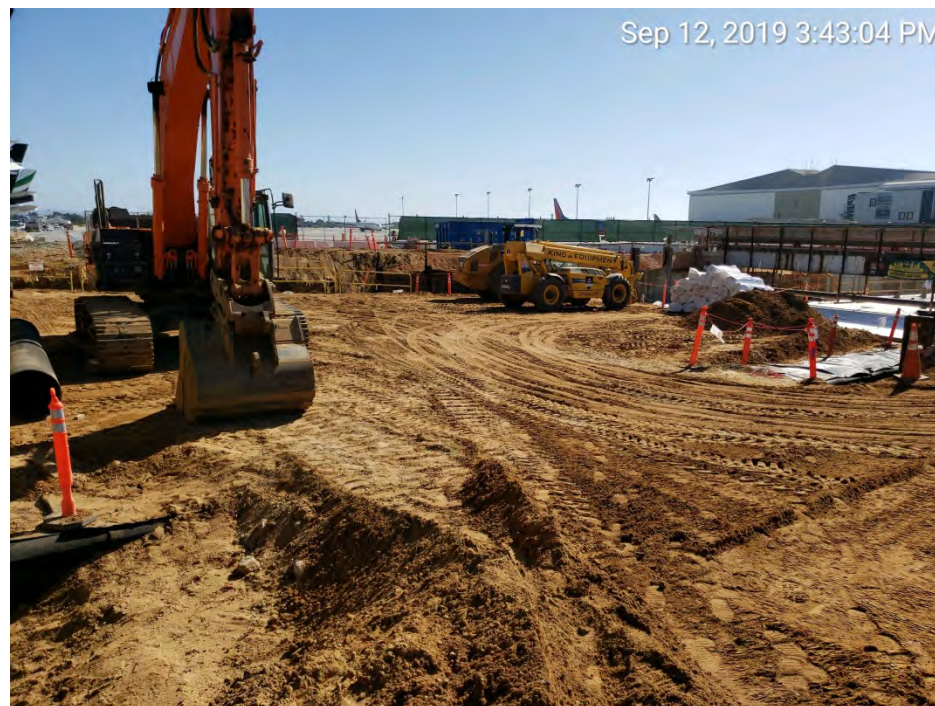


Sep 12, 2019 3:43:04 PM



Sep 13, 2019 9:43:19 AM



Sep 16, 2019 9:18:27 AM

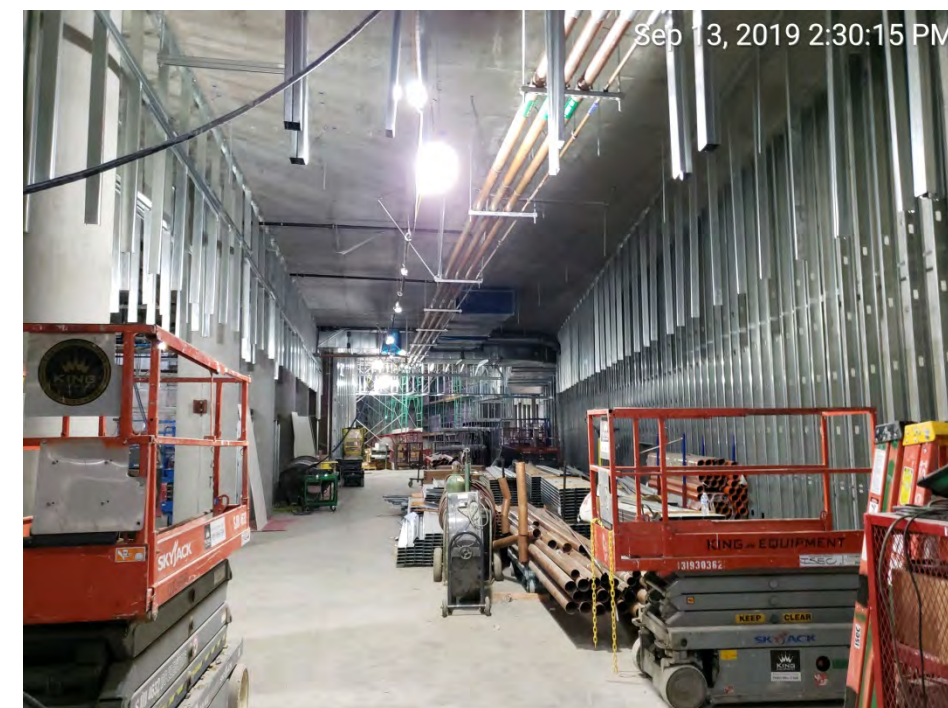



Sep 13, 2019 2:30:15 PM

General Updates:

- ☐ VI conveyor install continues
- ☐ AOA Security wall relocation
 - ☐ Turnover to VI 9/23
 - ☐ ACAMS activation 9/27
- ☐ Taxiway Airfield Paving
 - ☐ Continues

Upcoming Coordination:

- ☐ Temporary Service Road

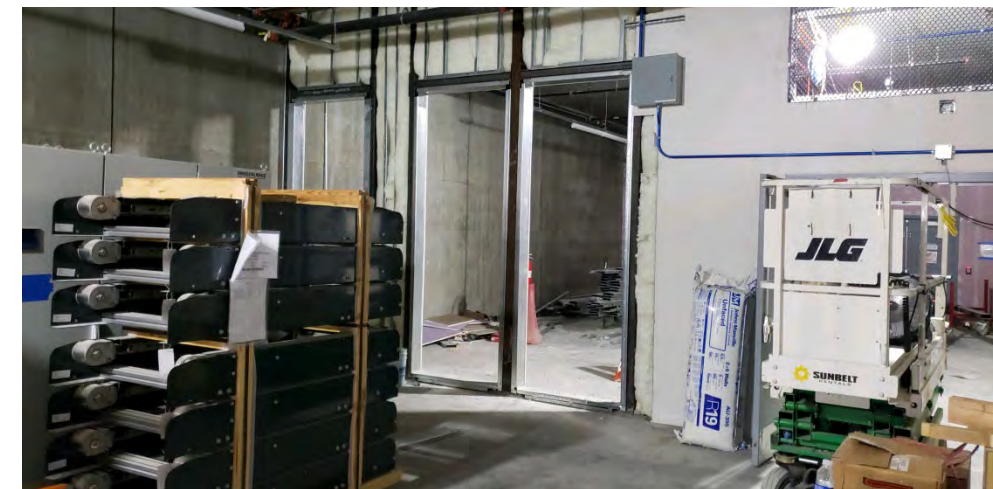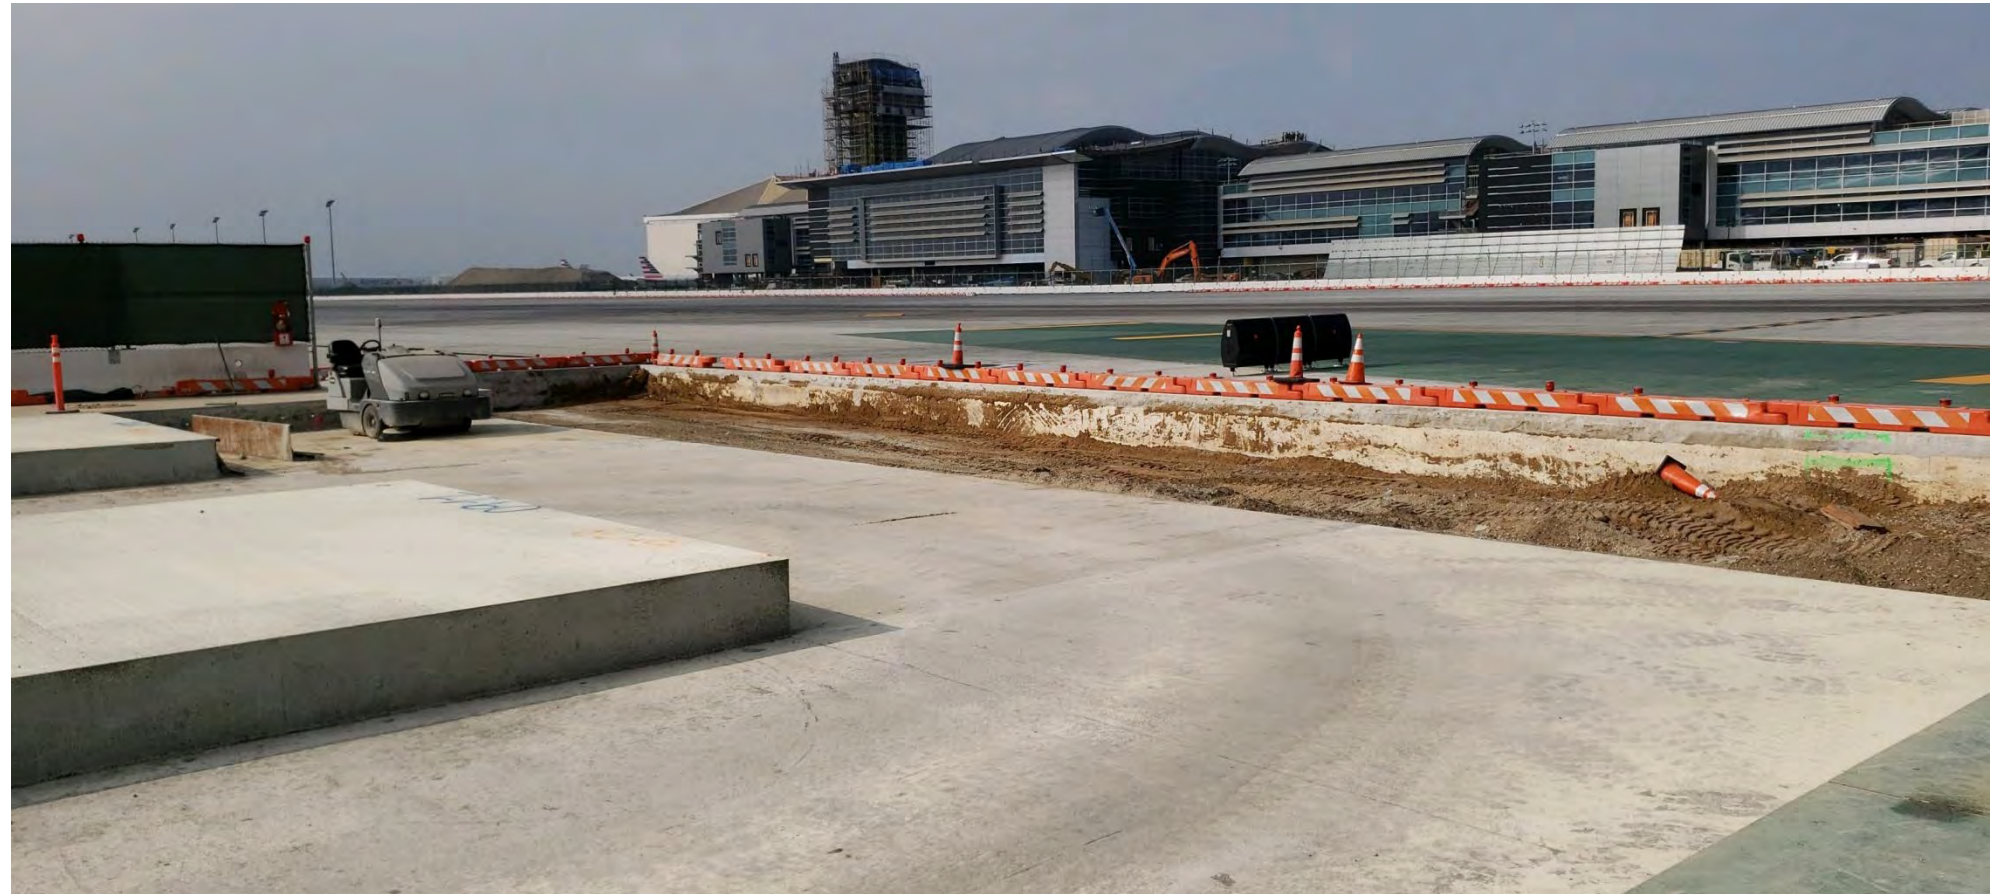


Utilidor Crossover Tunnel (Gate 132)

General Updates

- ☐ Electrical Room installation
- ☐ VI Continues BHS Install
- ☐ North tunnel Stub
 - ☐ Waterproofing complete
 - ☐ Backfill continues
- ☐ Utilities above tunnel continue
 - ☐ Sanitary Sewer
 - ☐ Storm Drain
 - ☐ Jet Fuel

Upcoming Coordination:

- ☐ Gate 134 Closure for Sanitary Sewer Clean-out (Tentative)

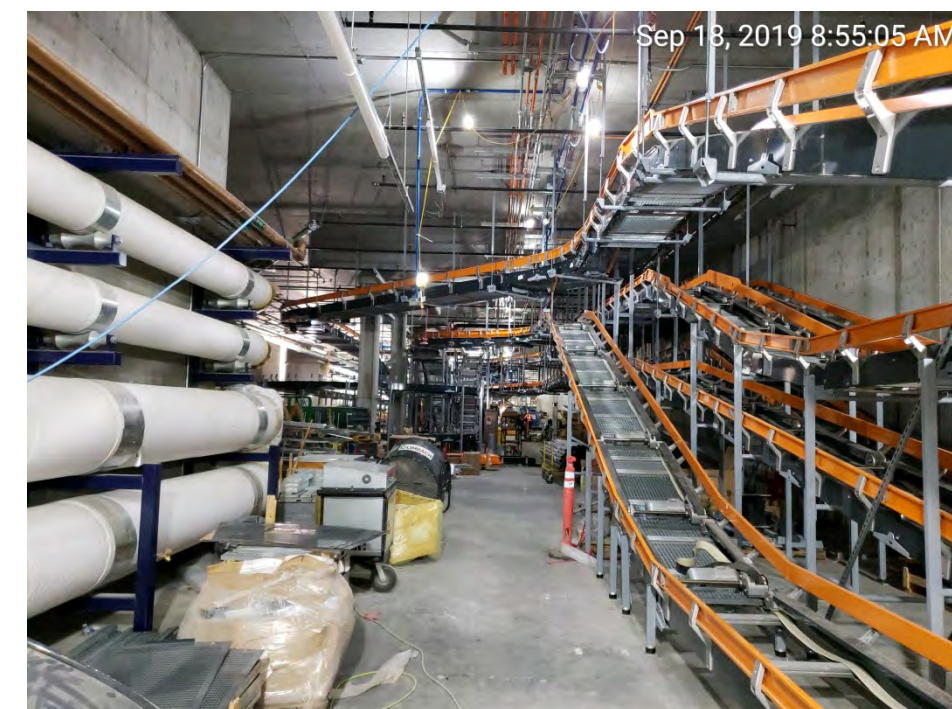

Updates by Geography

- ☐ MSC
 - ☐ Concourse
 - ☐ Civil
- ☐ Tunnels
 - ☐ TPAX
 - ☐ Utilidor
- ☒ Gateway
- ☐ BOP
 - ☐ BOP NBHS (IWBT)
 - ☐ BOP Far East Tunnel (Gate 131)
- ☐ BHS




Gateway - New Construction

General Update:

- ☐ Curtain Wall Install – South On-Going
- ☐ Interior Curtain Wall - Ongoing
- ☐ OH MEP Continues
- ☐ Electrical and IT Room Build Out
- ☐ T-Bar Grid at High Ceiling
- ☐ Apron flatwork Concrete Pour

Upcoming Coordination:

- ☐ Apron Paving Plan – 9/26

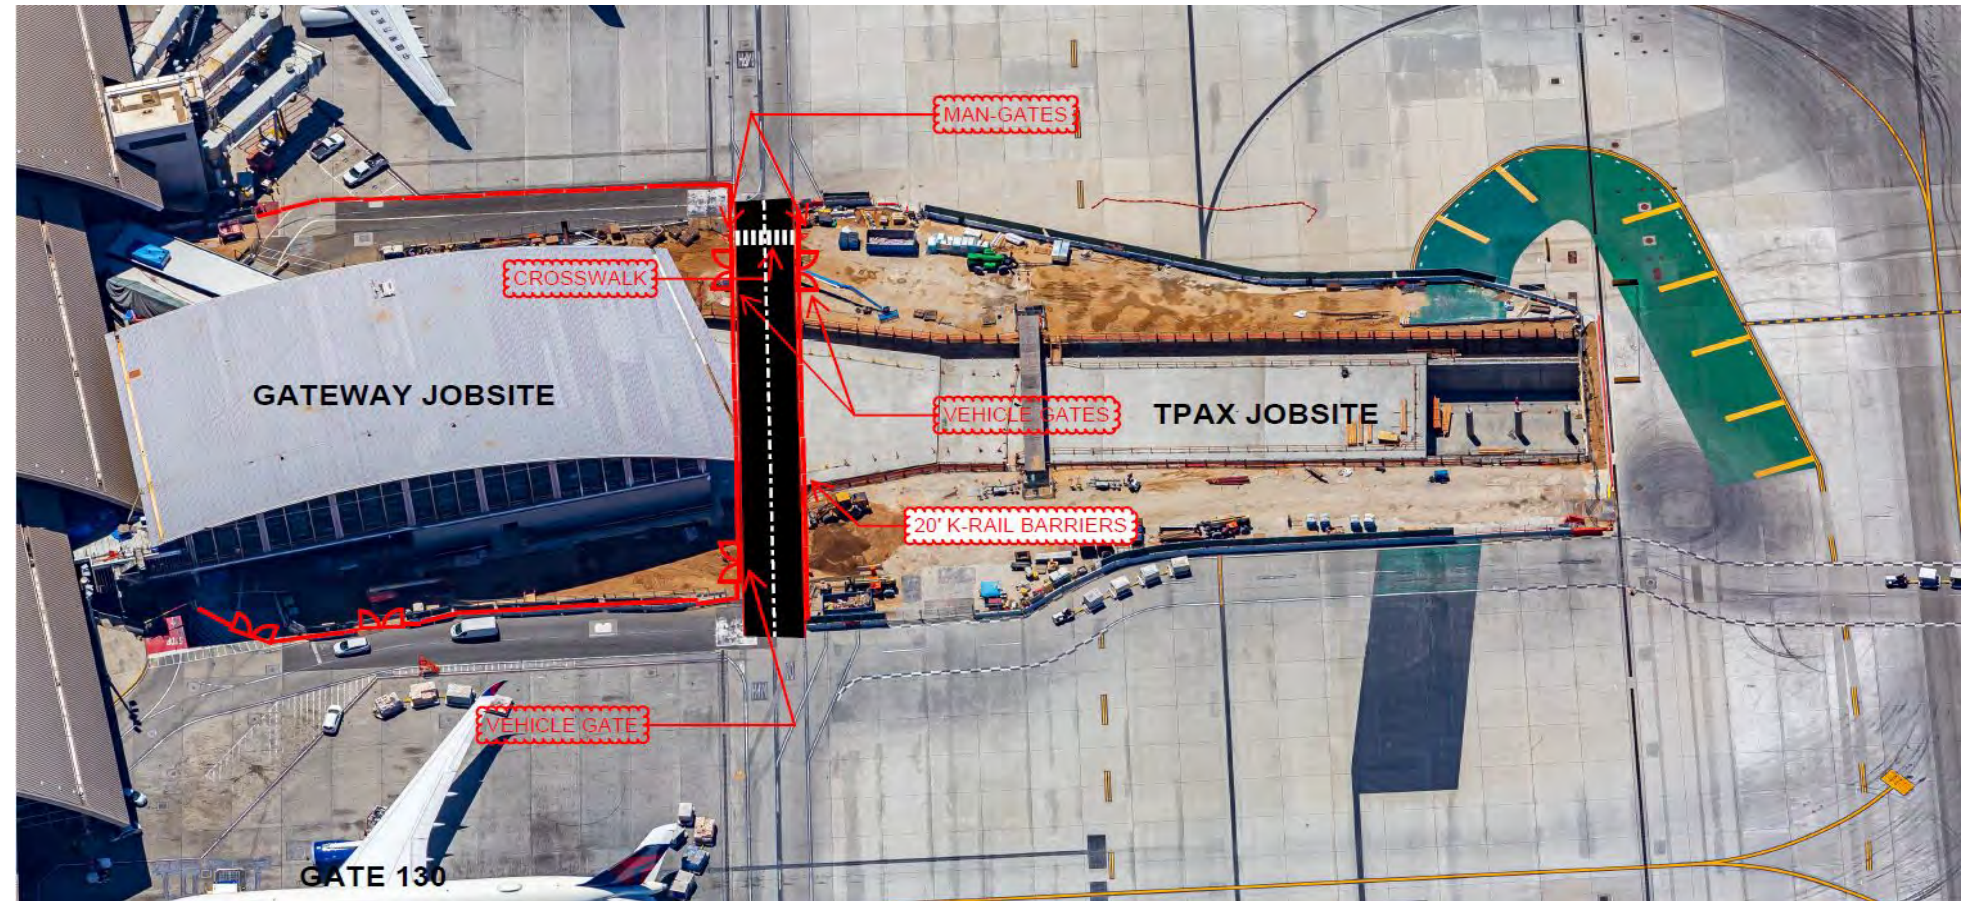



Gateway - Remodel Construction

General Update:

- ☐ NOCC – Coring at Interstitial Stairwell
 - ☐ Coring TBD
- ☐ Conveyor 10A – Electrical Mods
 - ☐ Scheduled Start 10/1

Upcoming Coordination:


- ☐ Chilled Water Tie-in Investigation
 - ☐ Upcoming

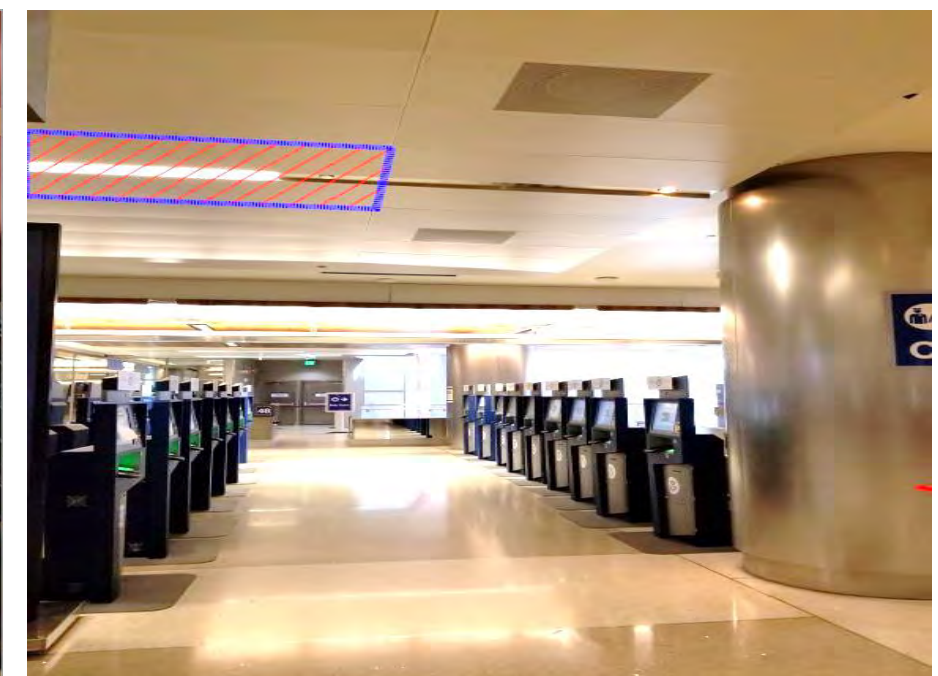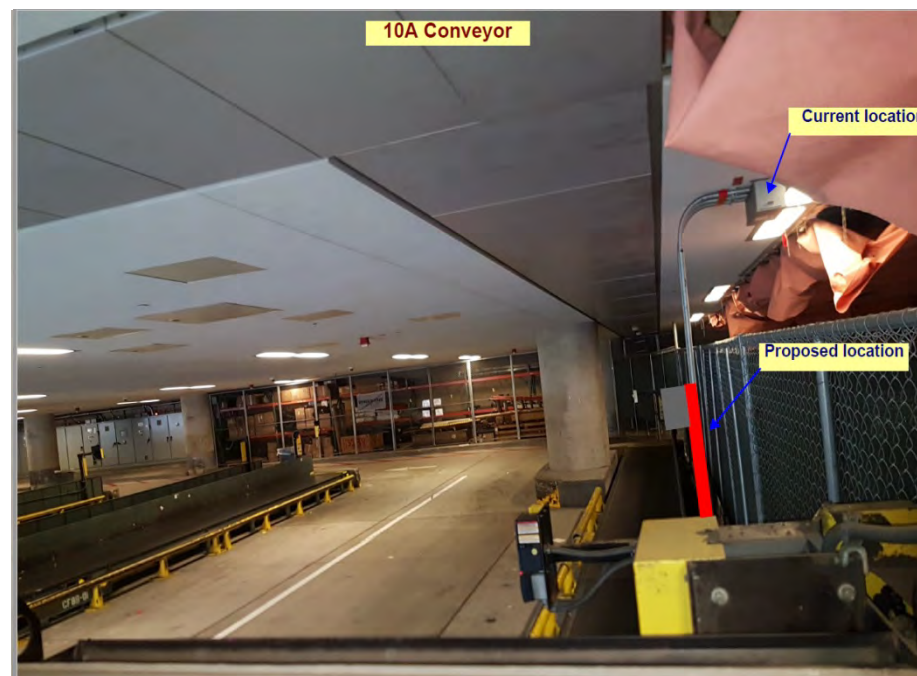

Gateway - Remodel Construction

Upcoming Coordination:

- ❑ ASR 4313 R7
 - ❑ The lane south of Gateway to be permanently closed.
 - ❑ West VSR lane to be reinstated
 - ❑ East VSR shall be for tug access only
 - ❑ Coordinating with OPS for final configuration

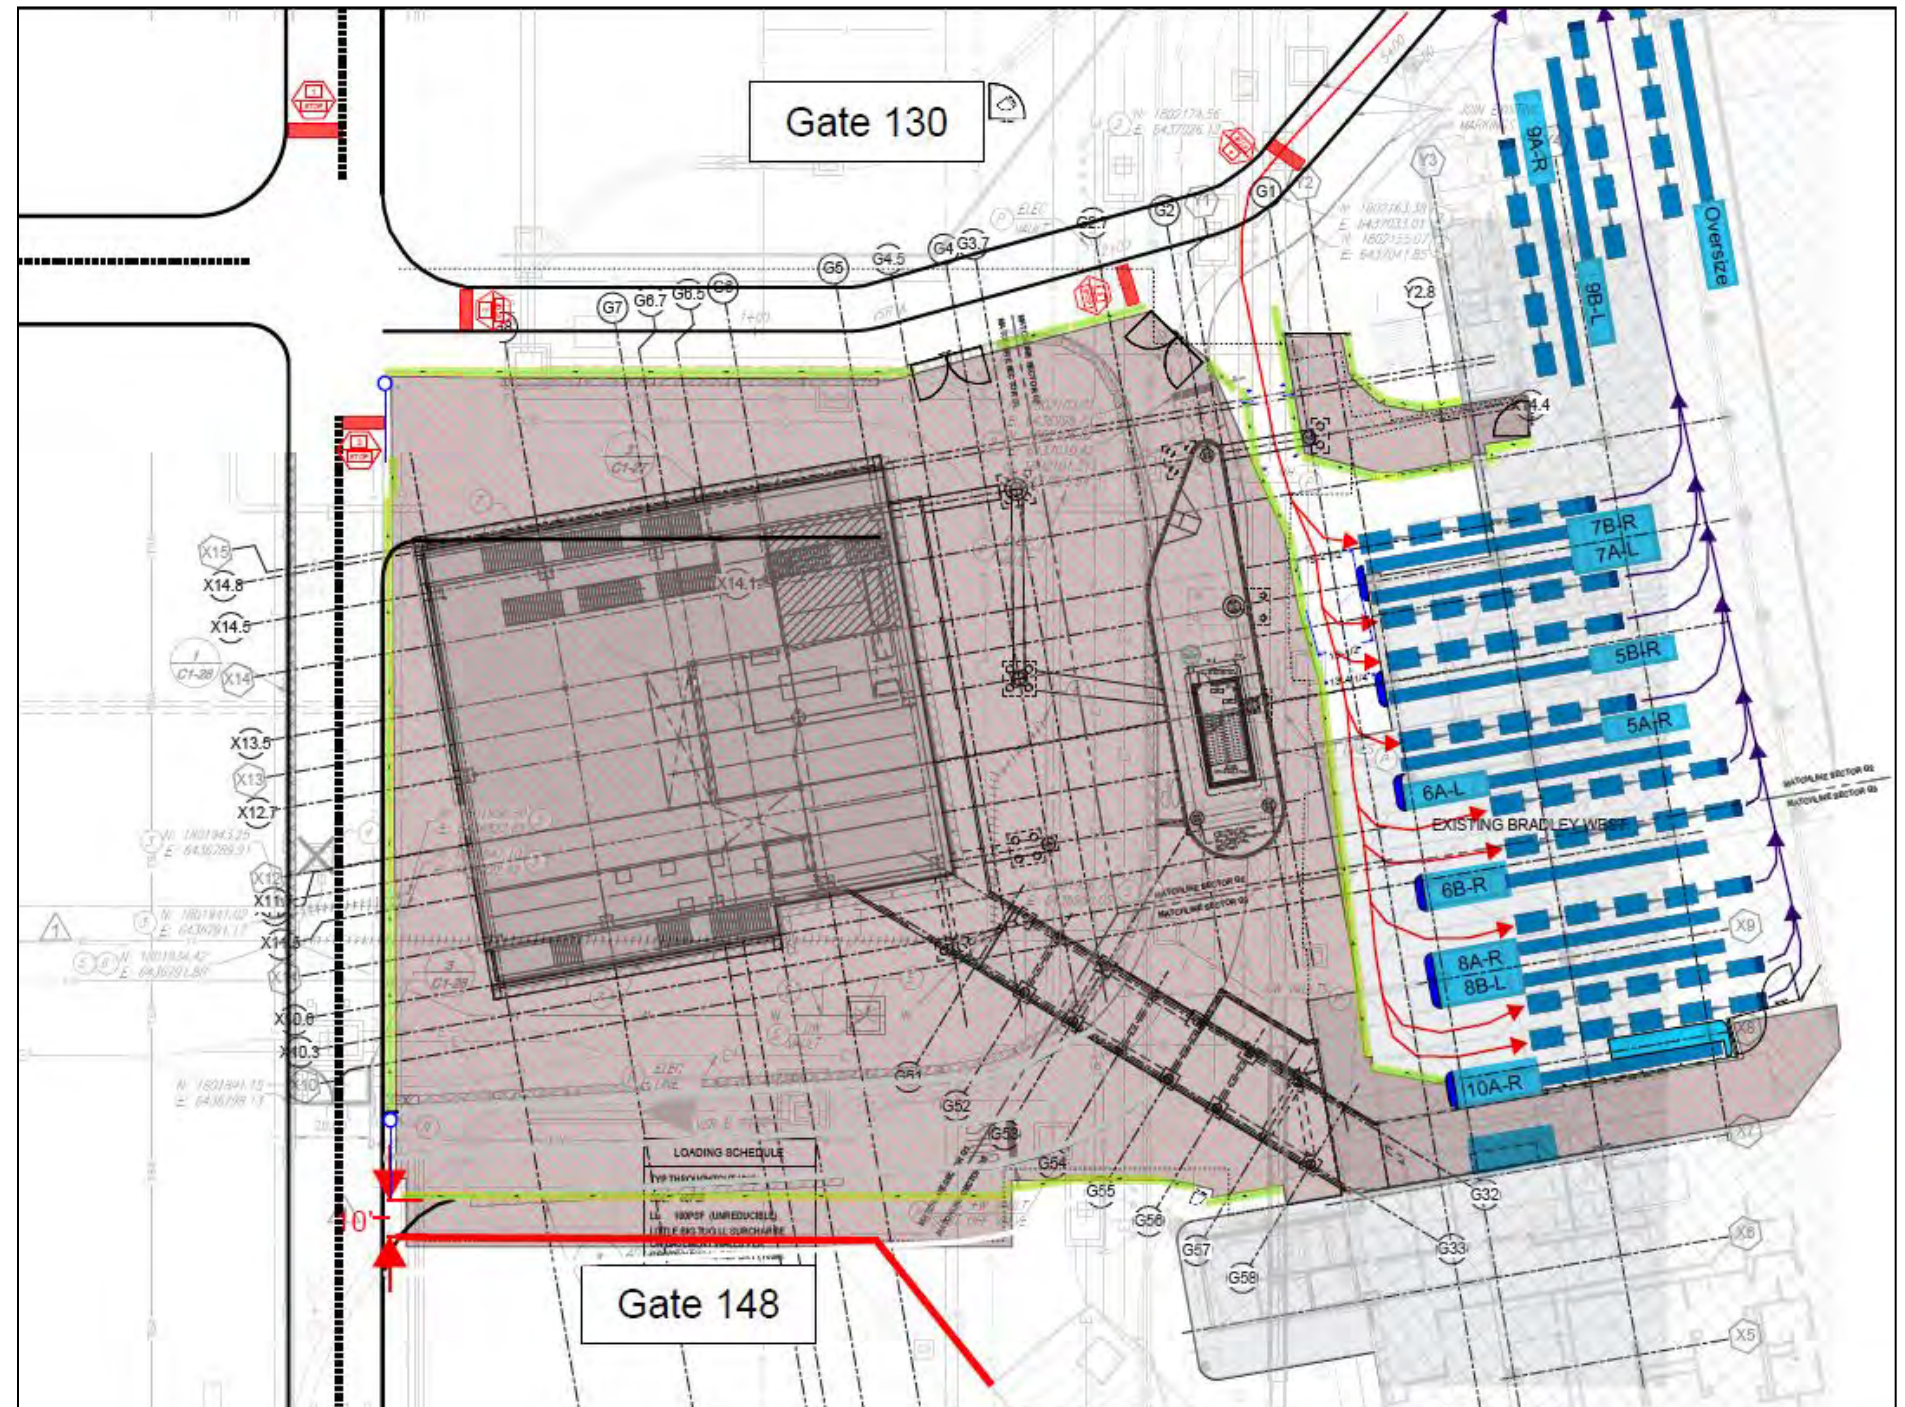

Updates by Geography

- ☐ MSC
 - ☐ Concourse
 - ☐ Civil
- ☐ Tunnels
 - ☐ TPAX
 - ☐ Utilidor
- ☐ Gateway
- ☐ BOP
 - ☐ BOP NBHS (IWBT)
 - ☐ BOP Far East Tunnel (Gate 131)
- ☐ BHS



General Updates:

- ❑ Bollards placed (East & West)
- ❑ Elevator Fronts – Complete
- ❑ Tie-in to Bradley for underground utilities
 - ❑ Communication Line
 - ❑ Vault Set – Thursday (9-18)
 - ❑ TBIT and NBHS connections on-going
 - ❑ Sewer Line
 - ❑ Restrooms point of connection
 - ❑ Domestic Water Line
 - ❑ Normal Power Shut down on-going

Upcoming Coordination:

- ❑ USR/ASR coordination for upcoming utility tie-ins
 - ❑ Power Shut Downs
 - ❑ Phase 2
 - ❑ Emergency Power
 - ❑ Normal Power



BOP Far East Tunnel (Gate 131)

General Update:

- ☐ Area 1
 - ☐ Site Utilities – Ongoing

- ☐ Area 2
 - ☐ Tunnel Backfill – Complete
 - ☐ MEP in the tunnel E2.4 - Ongoing
 - ☐ Site Utilities – Ongoing

- ☐ Area 3
 - ☐ CW/HW Piping Tie-in – Ongoing
 - ☐ TBIT Connector – Framing - Ongoing
 - ☐ TBIT Connector– Interior Finishing work - Ongoing



Upcoming Coordination:

- ☐ Chilled & Hot Water Piping Cutover

BOP Far East Tunnel (Gate 131)



Area 3 – CHW Line



Area 3 – CHW Flushing System

BOP Far East Tunnel (Gate 131)



Area 3 – TBIT Connector

BHS - MSC and West Tunnel

General Updates:

- ☐ Mechanical Installation:
 - ☐ West Tunnel - 95% (E)
 - ☐ MSC Basement - 99% (+1)
 - ☐ MSC Apron - 97% (+2)
- ☐ Electrical Installation:
 - ☐ East/West Tunnel - 30% (E)
 - ☐ MSC Apron/Basement - 53% (+12)
- ☐ Commissioning
 - ☐ MSC Apron/Basement - Pending

Upcoming Coordination:

- ☐ IT room access is being coordinated
- ☐ MSC site commissioning to begin next week
- ☐ Tunnel commissioning 12/04/2019

MSC Apron Conveyor



General Updates:

☐ Mechanical Installation:

- ☐ NBHS Basement - 90% (+5)
- ☐ NBHS Apron - 82% (+3)
- ☐ Mixing Box - 40% (+2)
- ☐ East Tunnel - 92% (-4)
- ☐ Crossover - 27% (+15)
- ☐ Far East - 53% (+15)

☐ Electrical Installation:

- ☐ NBHS Apron/Basement - 1% (E)
- ☐ Cross/Chute/FET/Mixing Box - TBD

Upcoming Coordination:

U3 Fire/Security Door - 9/23/2019

TBIT Connector Access point - 11/02/2019


Overall Complete:

Mechanical – 73.14% (+1.07)


Electrical – 18.9% (+2.9)

NBHS Apron Make-up Belts





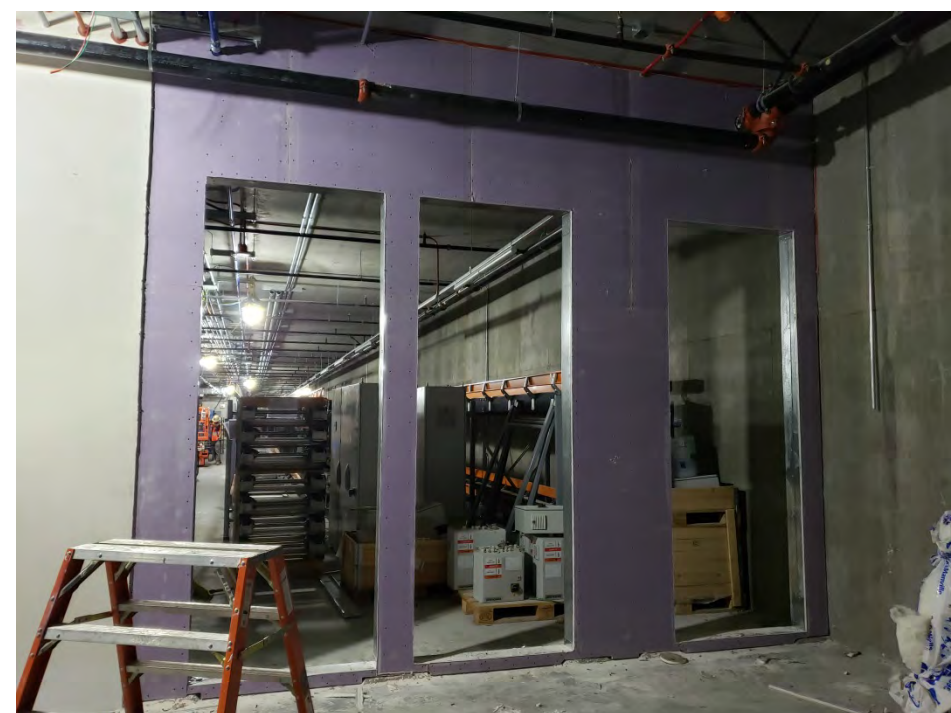


East/West Utilidor Fire Door



Far East Tunnel

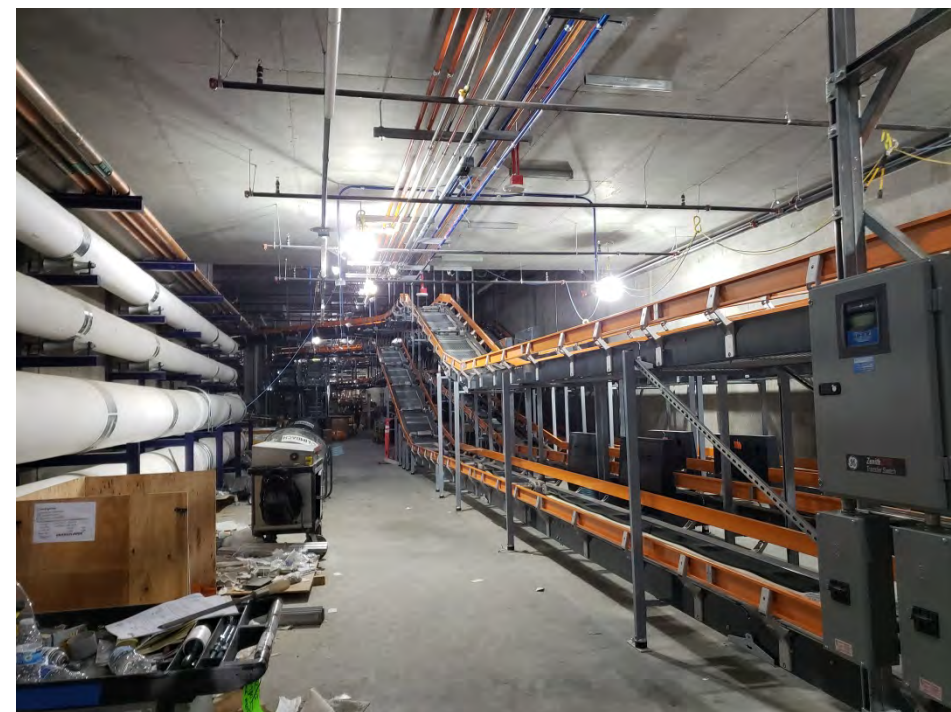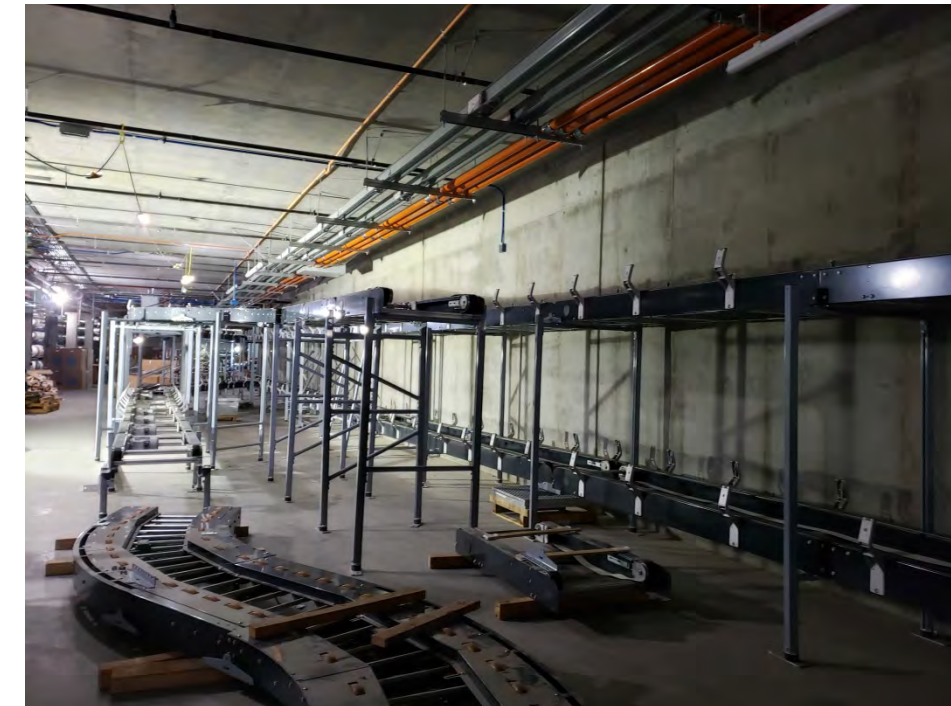


East Utilidor




Airforce One



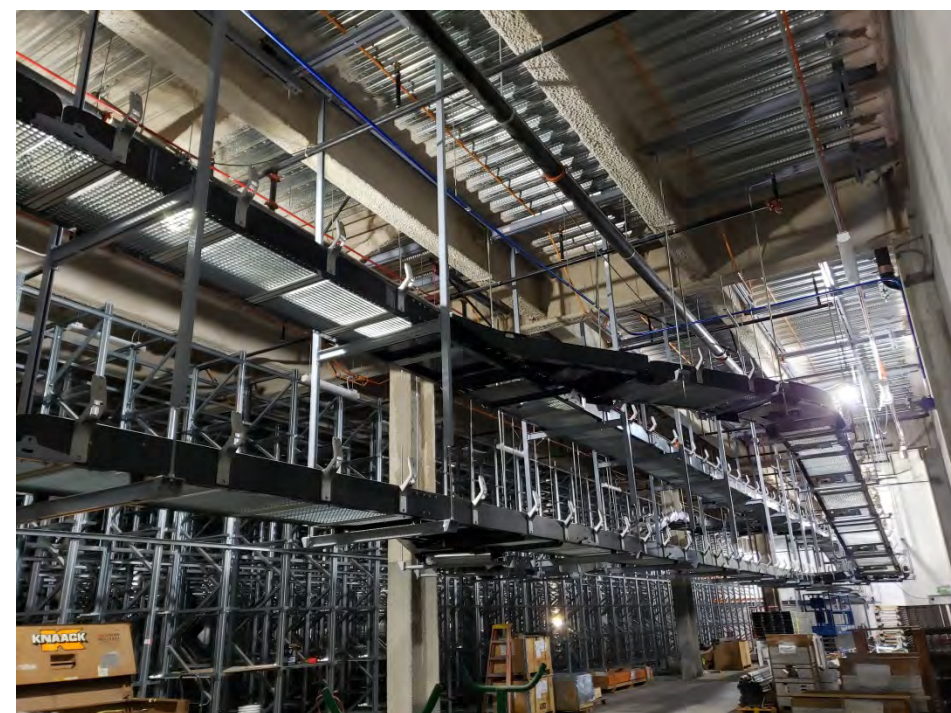


NBHS Basement



Crossover Tunnel



NBHS Apron



Crossover Tunnel



Maintenance Access Update

General Update:



- ❑ MSC Basement Level:
 - ❑ 50 % Completed
 - ❑ Open: 0 Closed: 0

- ❑ MSC Concourse Level:
 - ❑ 40% Complete
 - ❑ Open: 20 Closed: 32

MSC Basement Level



MSC Concourse Level

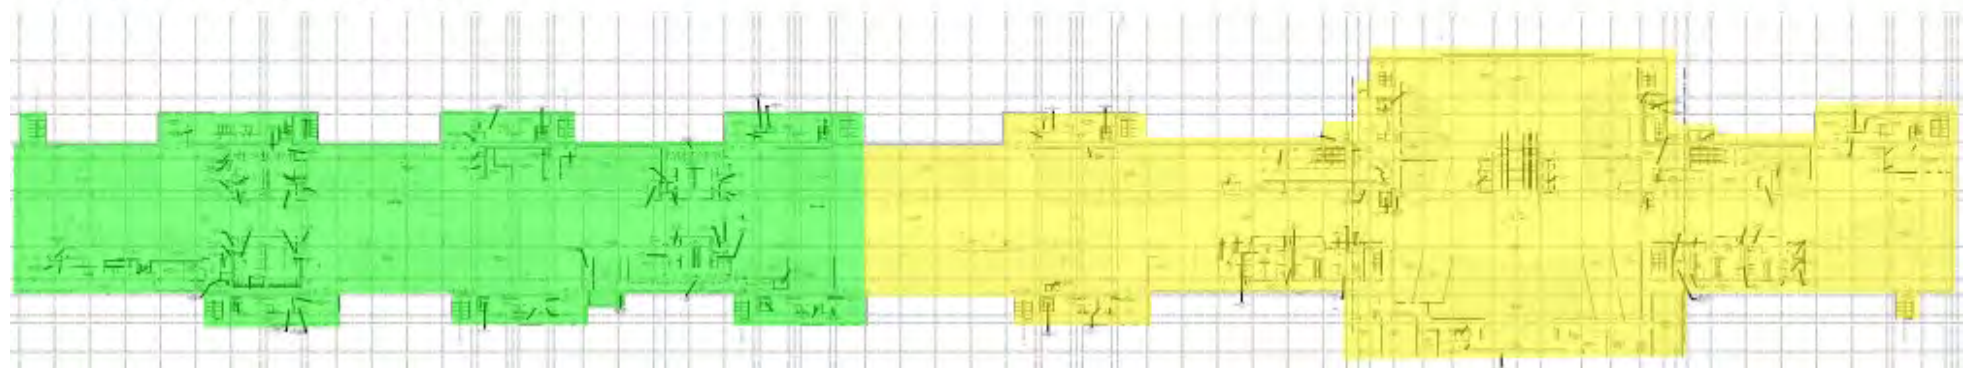


Maintenance Access Update

General Update:


- ❑ MSC Apron Level:
 - ❑ 40% Complete
 - ❑ Open: 12 Closed: 9



- ❑ MSC Sterile Level:
 - ❑ 50% Complete
 - ❑ Open: 0 Closed: 1

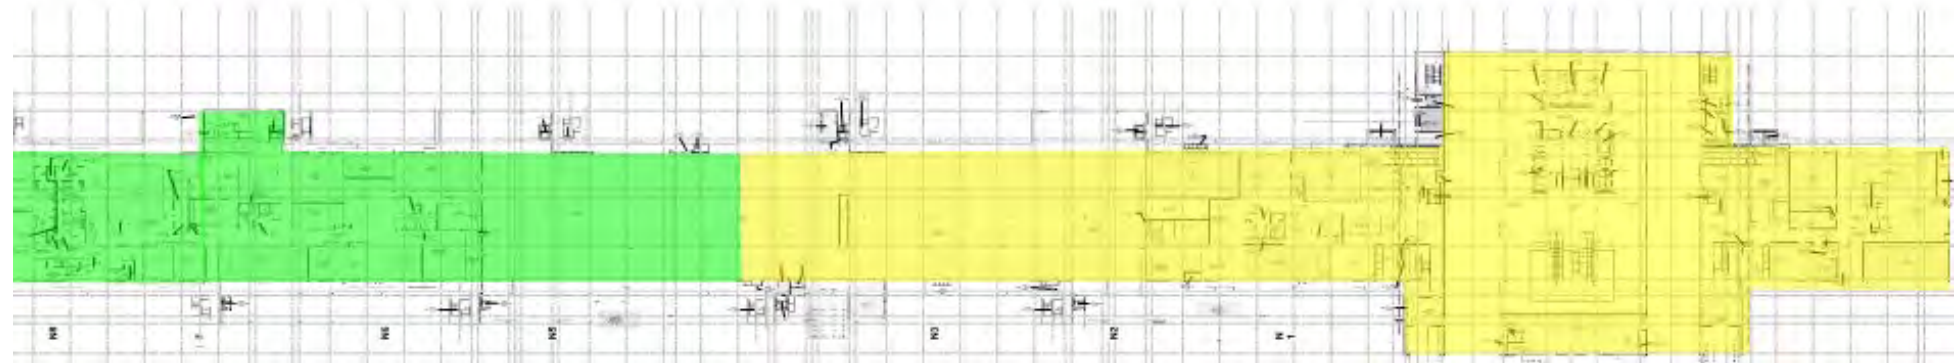MSC Apron Level

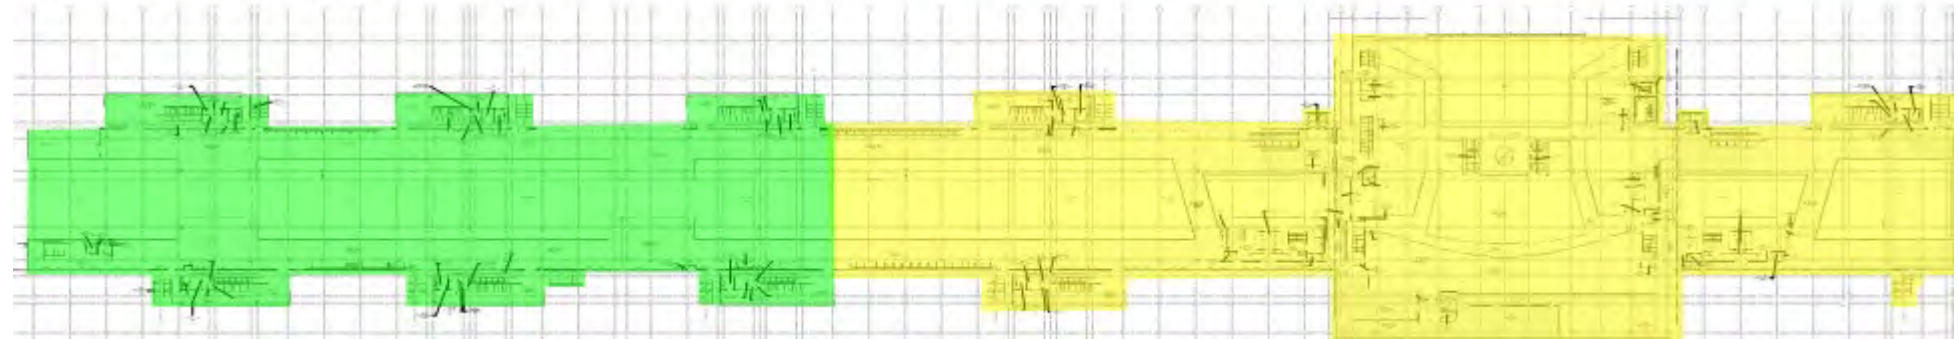

MSC Sterile Level



-  Areas Walked
-  Areas To Be Walked


Maintenance Access Update

General Update:


- ☐ Gateway – All Levels:
 - ☐ 0% Complete
 - ☐ Open: TBD Closed: TBD

- ☐ PAX Tunnel:
 - ☐ 40% Complete
 - ☐ Open:0 Closed:0

Gateway – All Levels

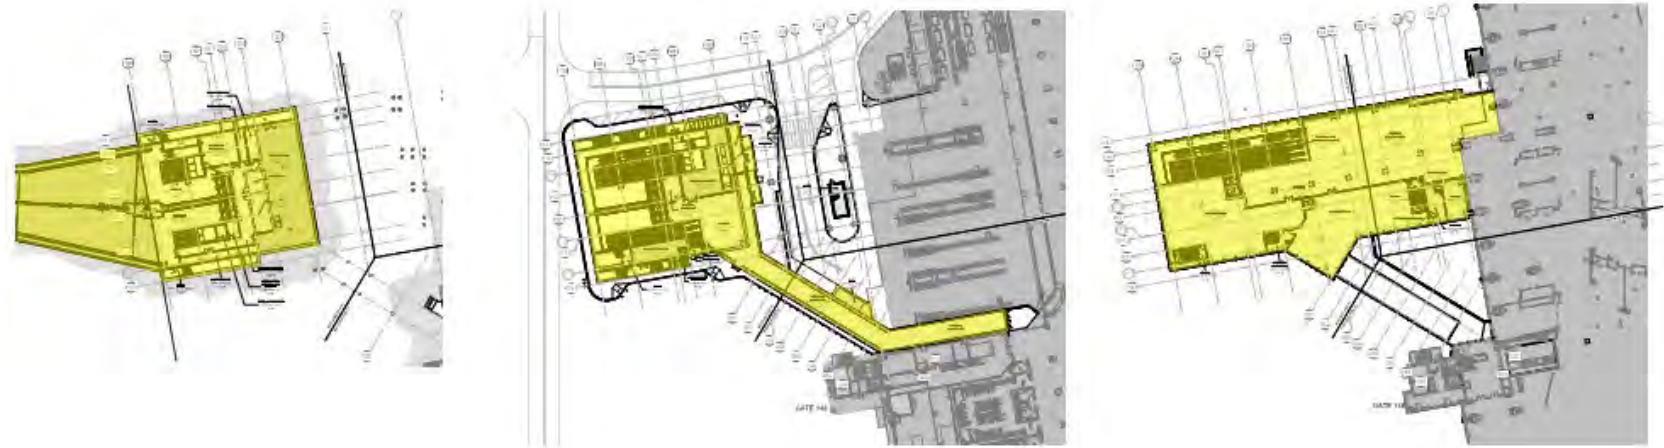

PAX Tunnel

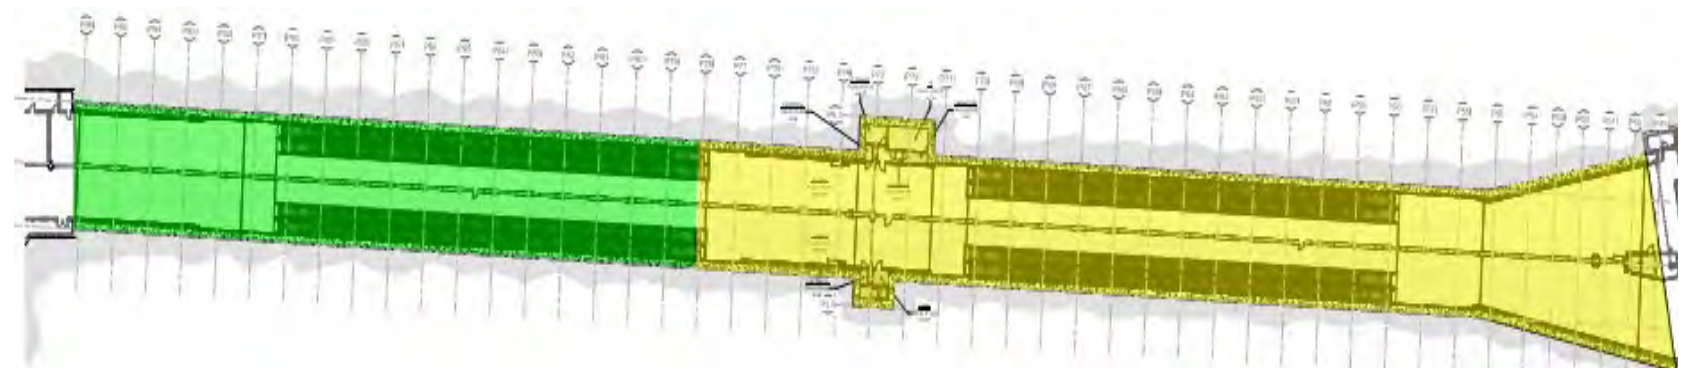

- ☐ Areas Walked
- ☐ Areas To Be Walked


Maintenance Access Update

General Update:


- ☐ NBHS – All Levels:
 - ☐ 100% Complete
 - ☐ Open: 0 Closed: 0

- ☐ LADWP:
 - ☐ 0% Complete
 - ☐ Open: 0 Closed: 1

NBHS – All Levels

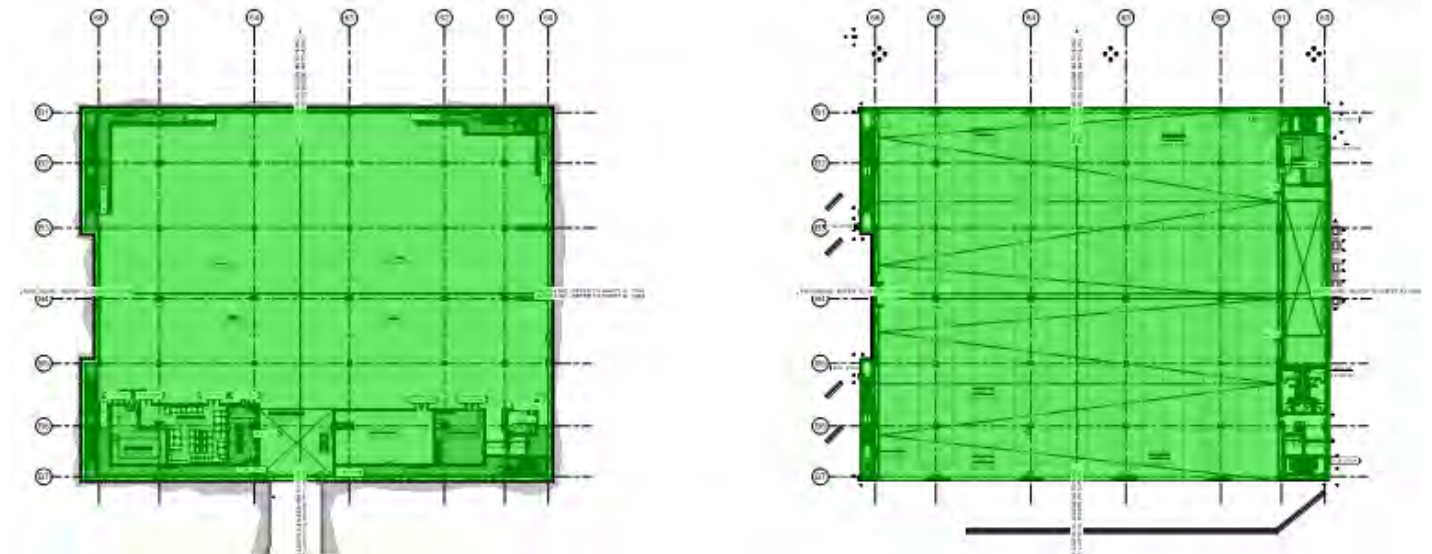

LADWP

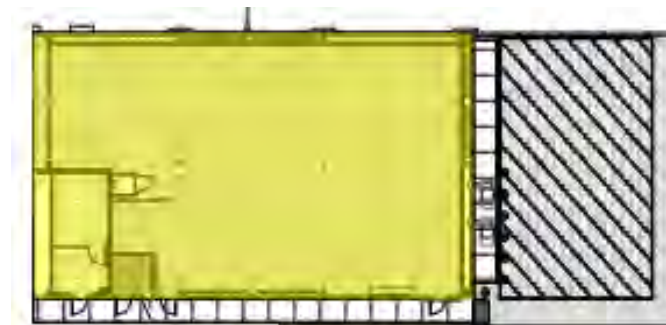

- ☐ Areas Walked
- ☐ Areas To Be Walked

Maintenance Access Update


General Update:

- ☐ Utility Tunnel:
 - ☐ 0% Complete
 - ☐ Open: TBD Closed: TBD
- ☐ TUTL – E:
 - ☐ 0% Complete
 - ☐ Open: TBD Closed: TBD

Upcoming Coordination:

- ☐ 9/25/2019: Walk Utilidor West
- ☐ 10/02/2019: Walk Concourse N3 - N1
- ☐ 10/9/2019: Walk Apron N4 – N1

Utility Tunnel

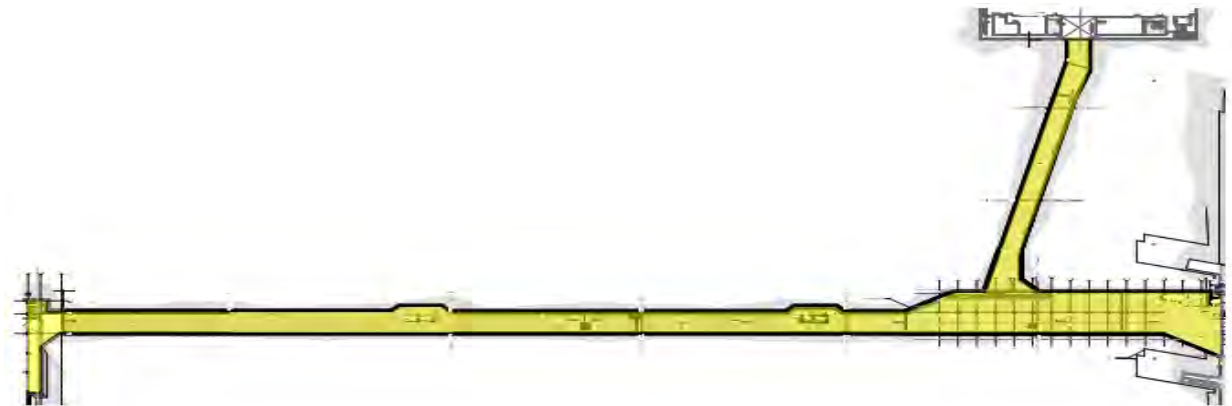

TUTL - E



- ☐ Areas Walked
- ☐ Areas To Be Walked

In Works:

- ☐ CBP / TSA - In-Transit Passenger Processing - DCN 115
- ☐ GIDSs Advertising Modifications
- ☐ Children's Play Area
- ☐ Back-of-house FF&E Needs
- ☐ Self-Boarding/E-Gates - boarding area
- ☐ Ramp Control Tower Implementation Phase

IT


- ☐ Interactive Displays Millwork Design
- ☐ DAS Cellular & 5G








Recurring


- | | |
|--|------------------------|
| <input type="checkbox"/> Ramp Control Tower | Weekly Tues |
| <input type="checkbox"/> Maintenance Access Walks | Weekly Wed |
| <input type="checkbox"/> Concessions Coordination | Weekly Thurs |
| <input type="checkbox"/> AOR FIT for Airlines | Weekly Thurs |
| <input type="checkbox"/> BHS Coordination | Weekly Fri |
| <input type="checkbox"/> AOR Volunteer Outreach | Bi-Weekly Tues |
| <input type="checkbox"/> AOR FMUG Working Group | Bi-Weekly Thurs |
| <input type="checkbox"/> AOR RCT Focus Group | Bi-Weekly Thurs |
| <input type="checkbox"/> Risk Management Collaboration | Bi-Weekly Fri |
| <input type="checkbox"/> BHS Schedule | Last Wed of each month |
| <input type="checkbox"/> BHS Recovery Coordination | Weekly Wed |

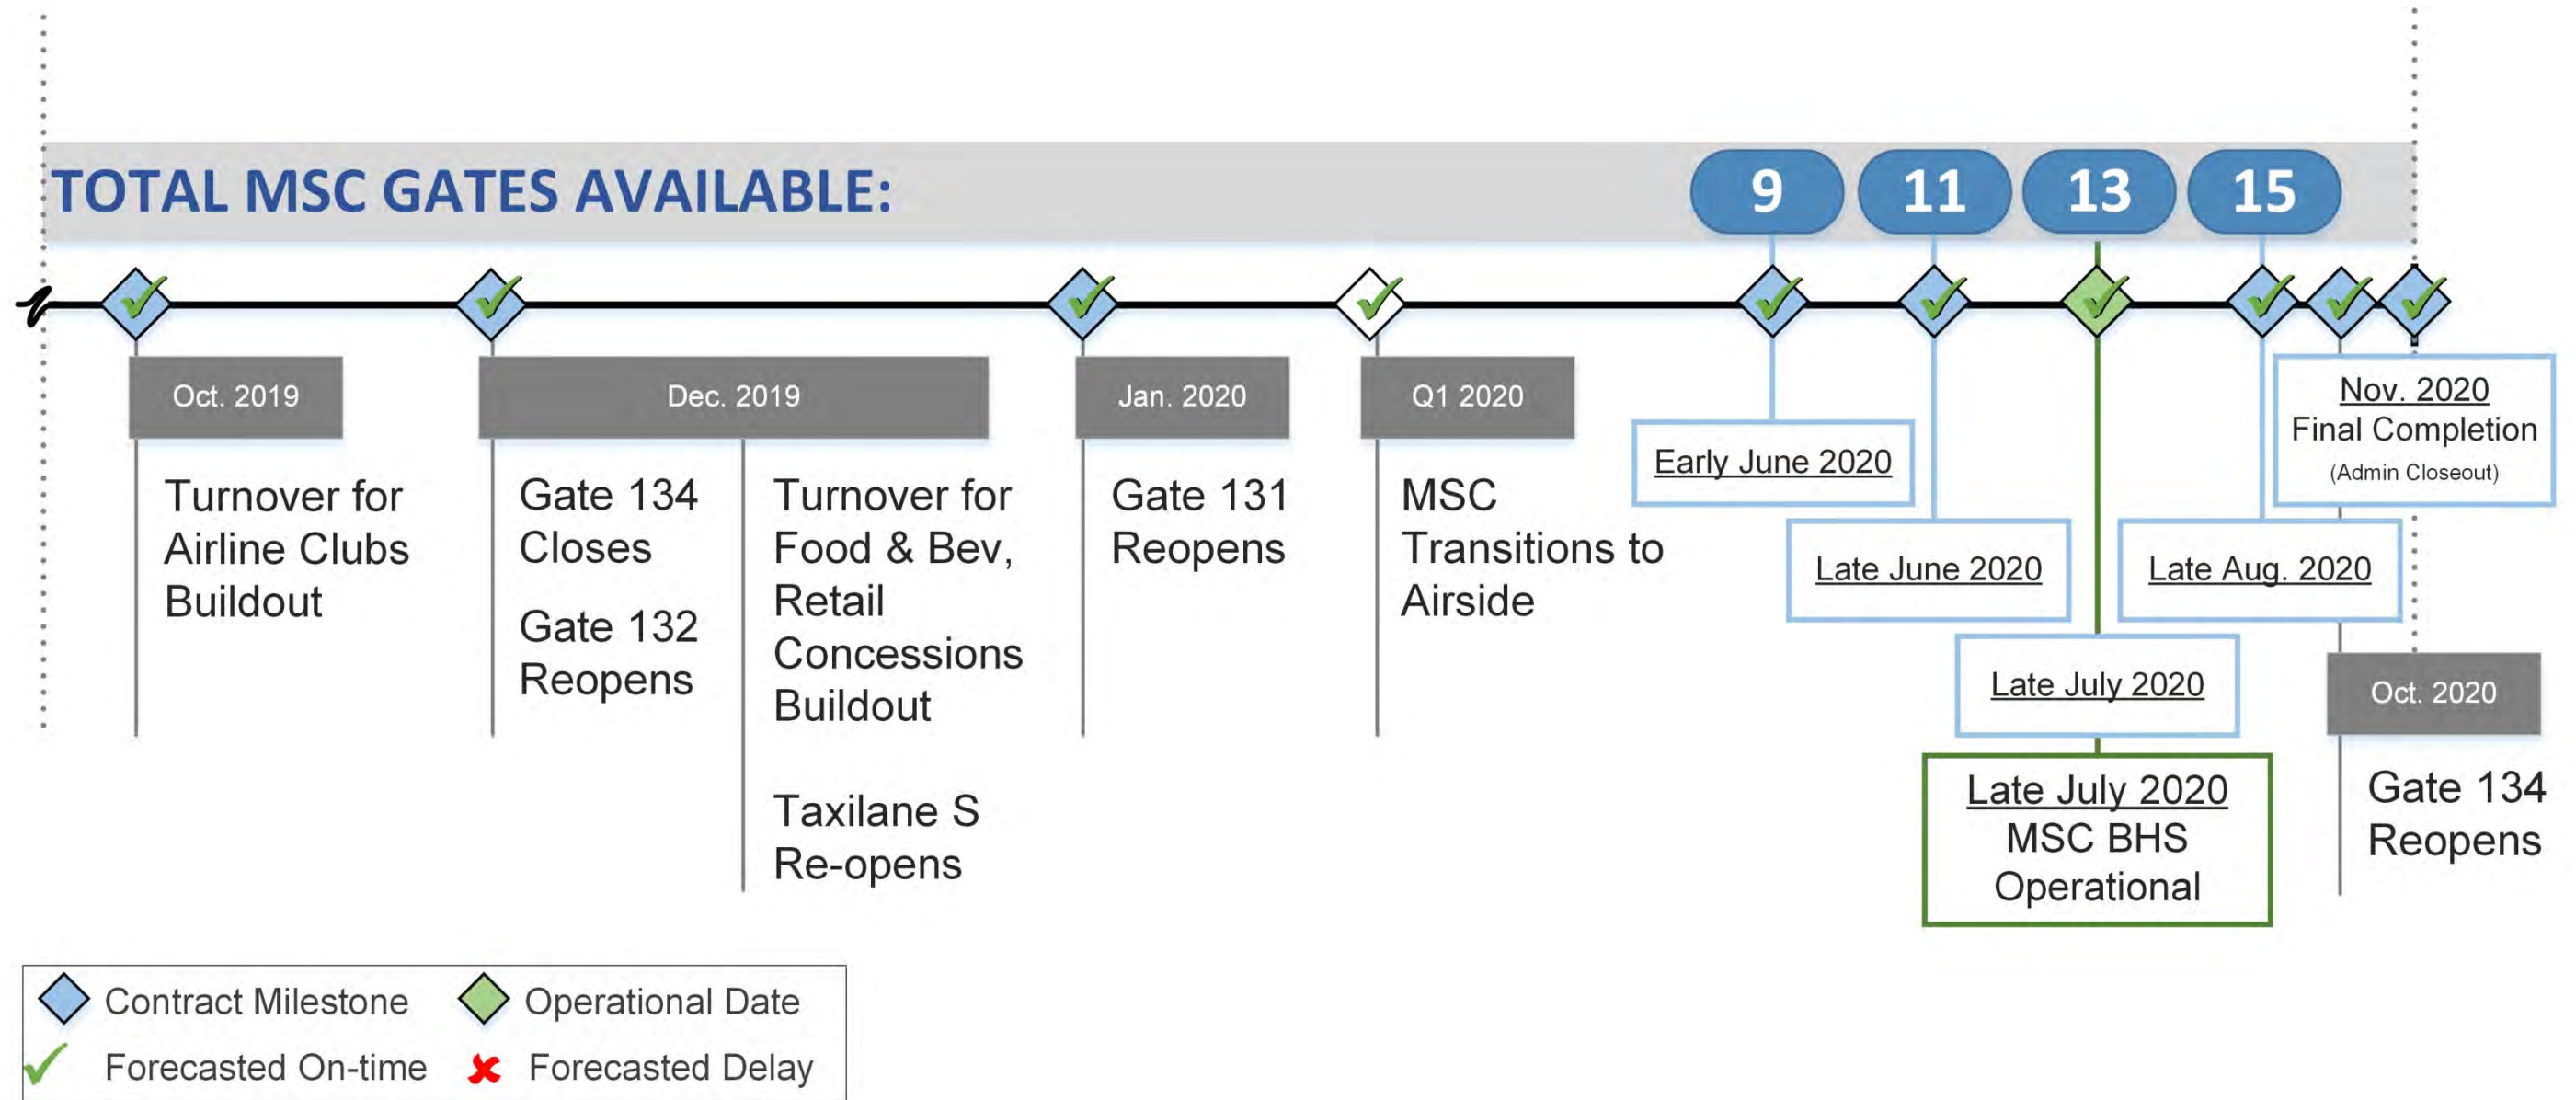

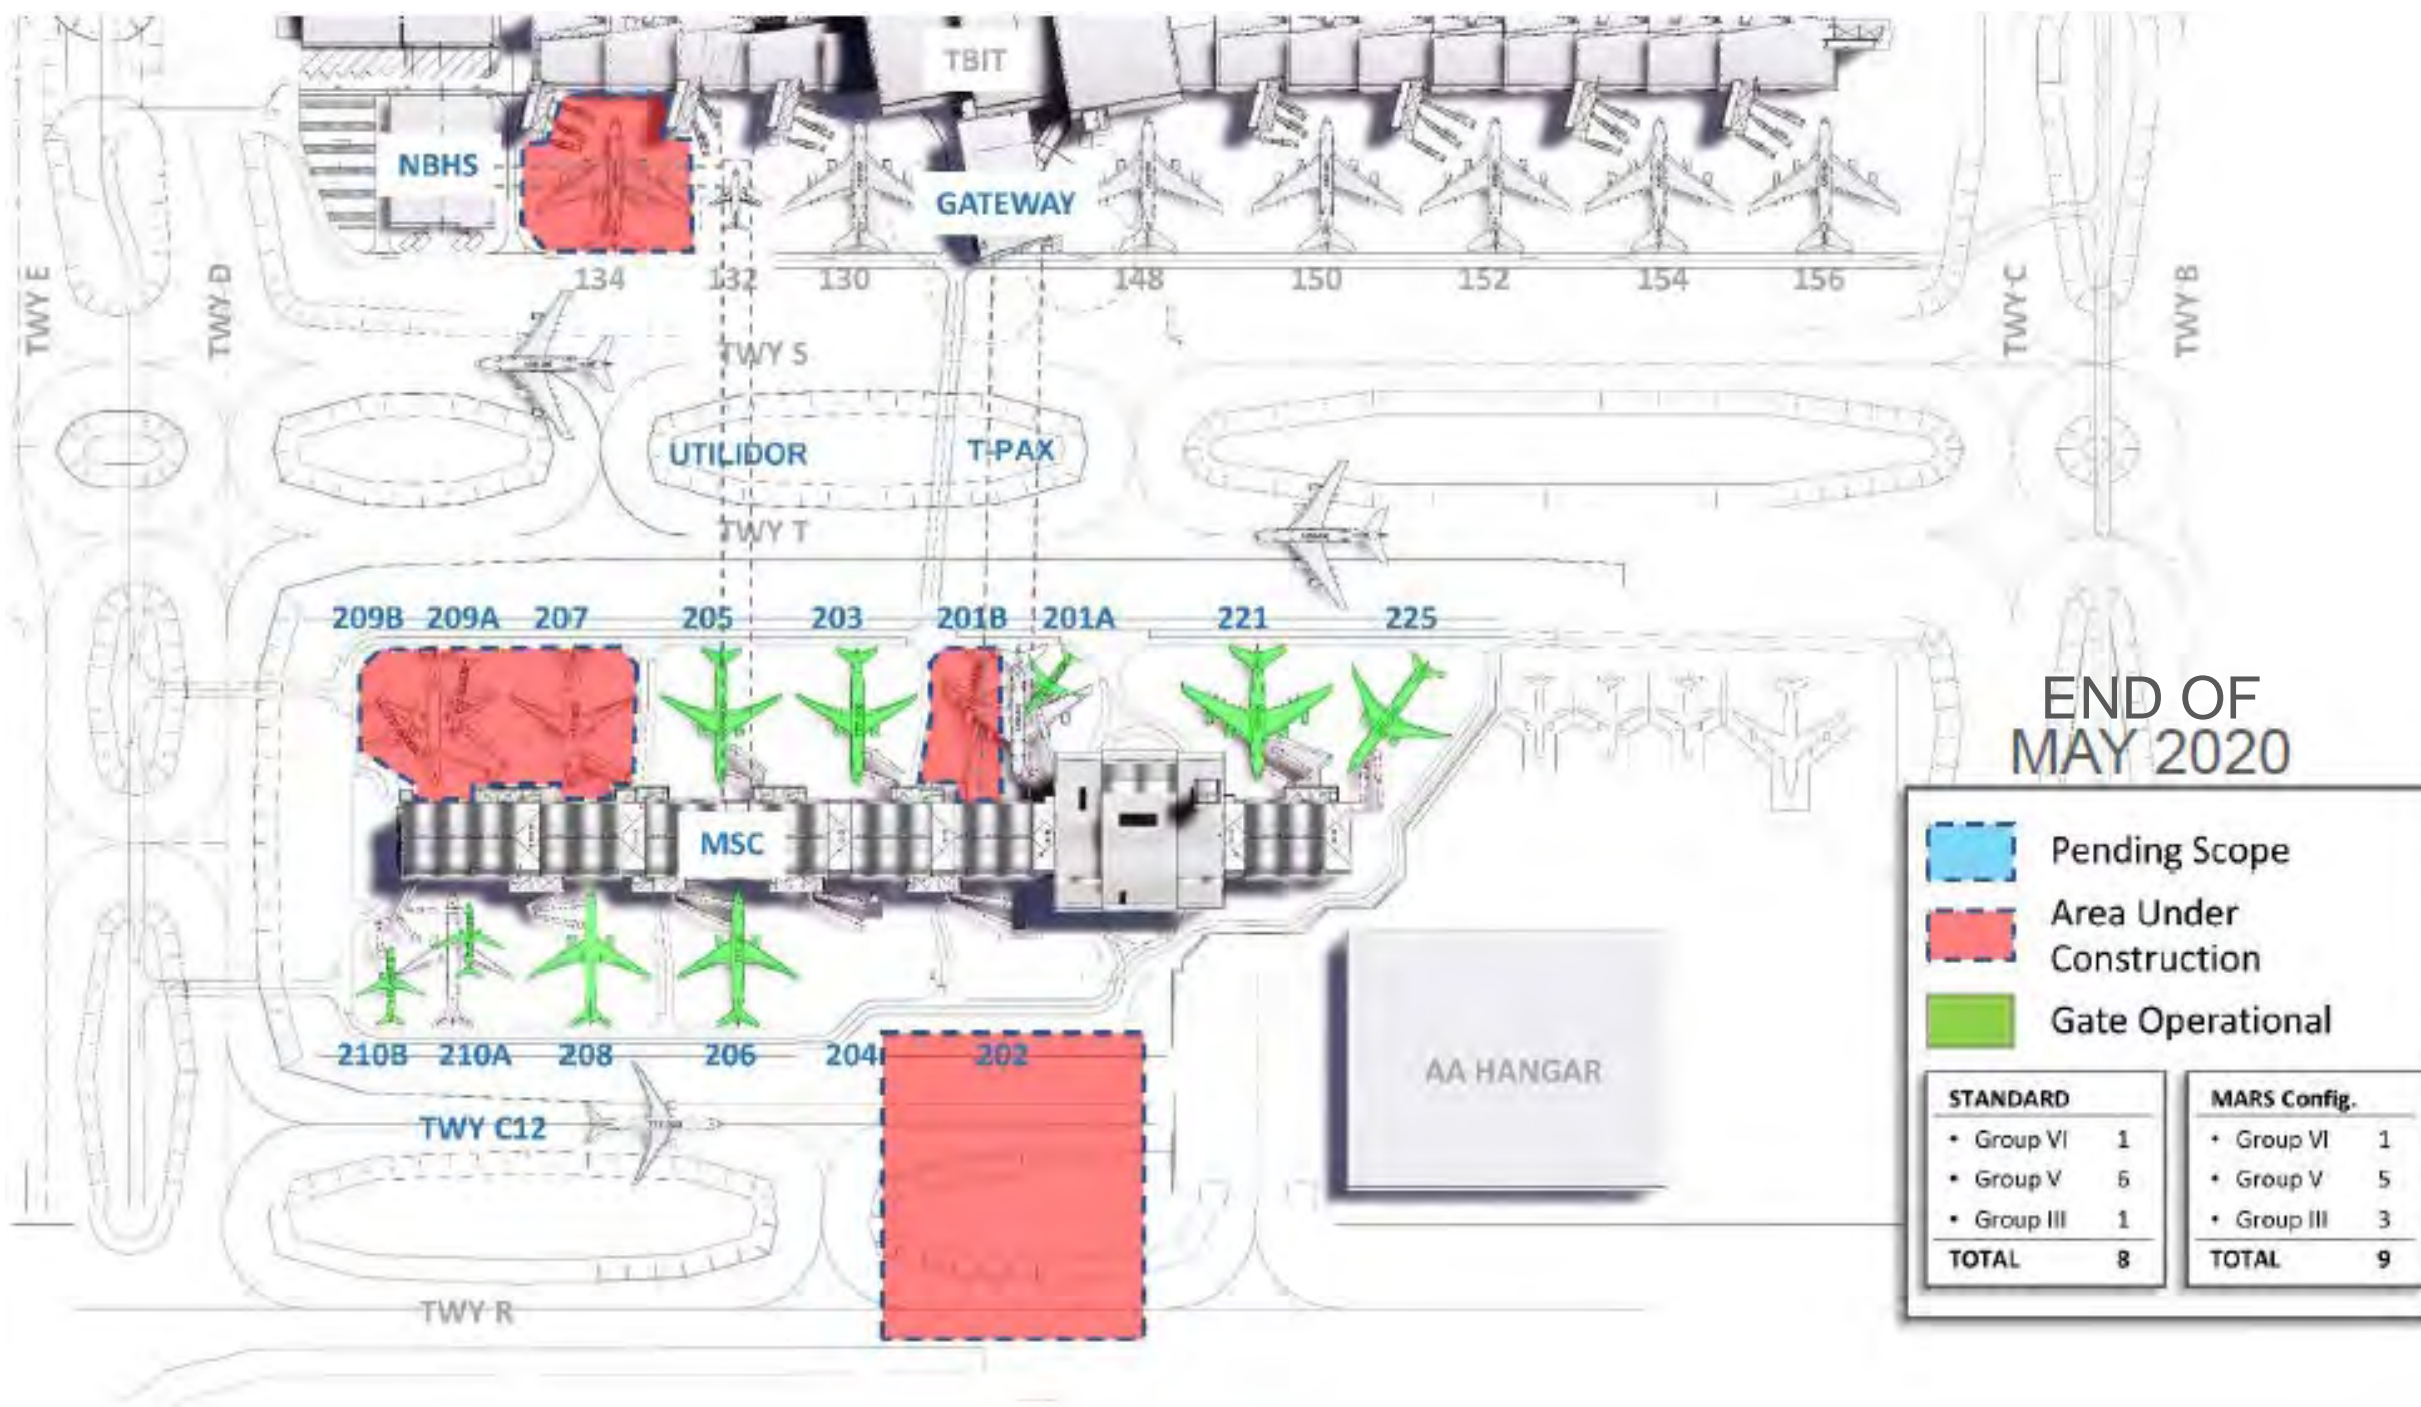

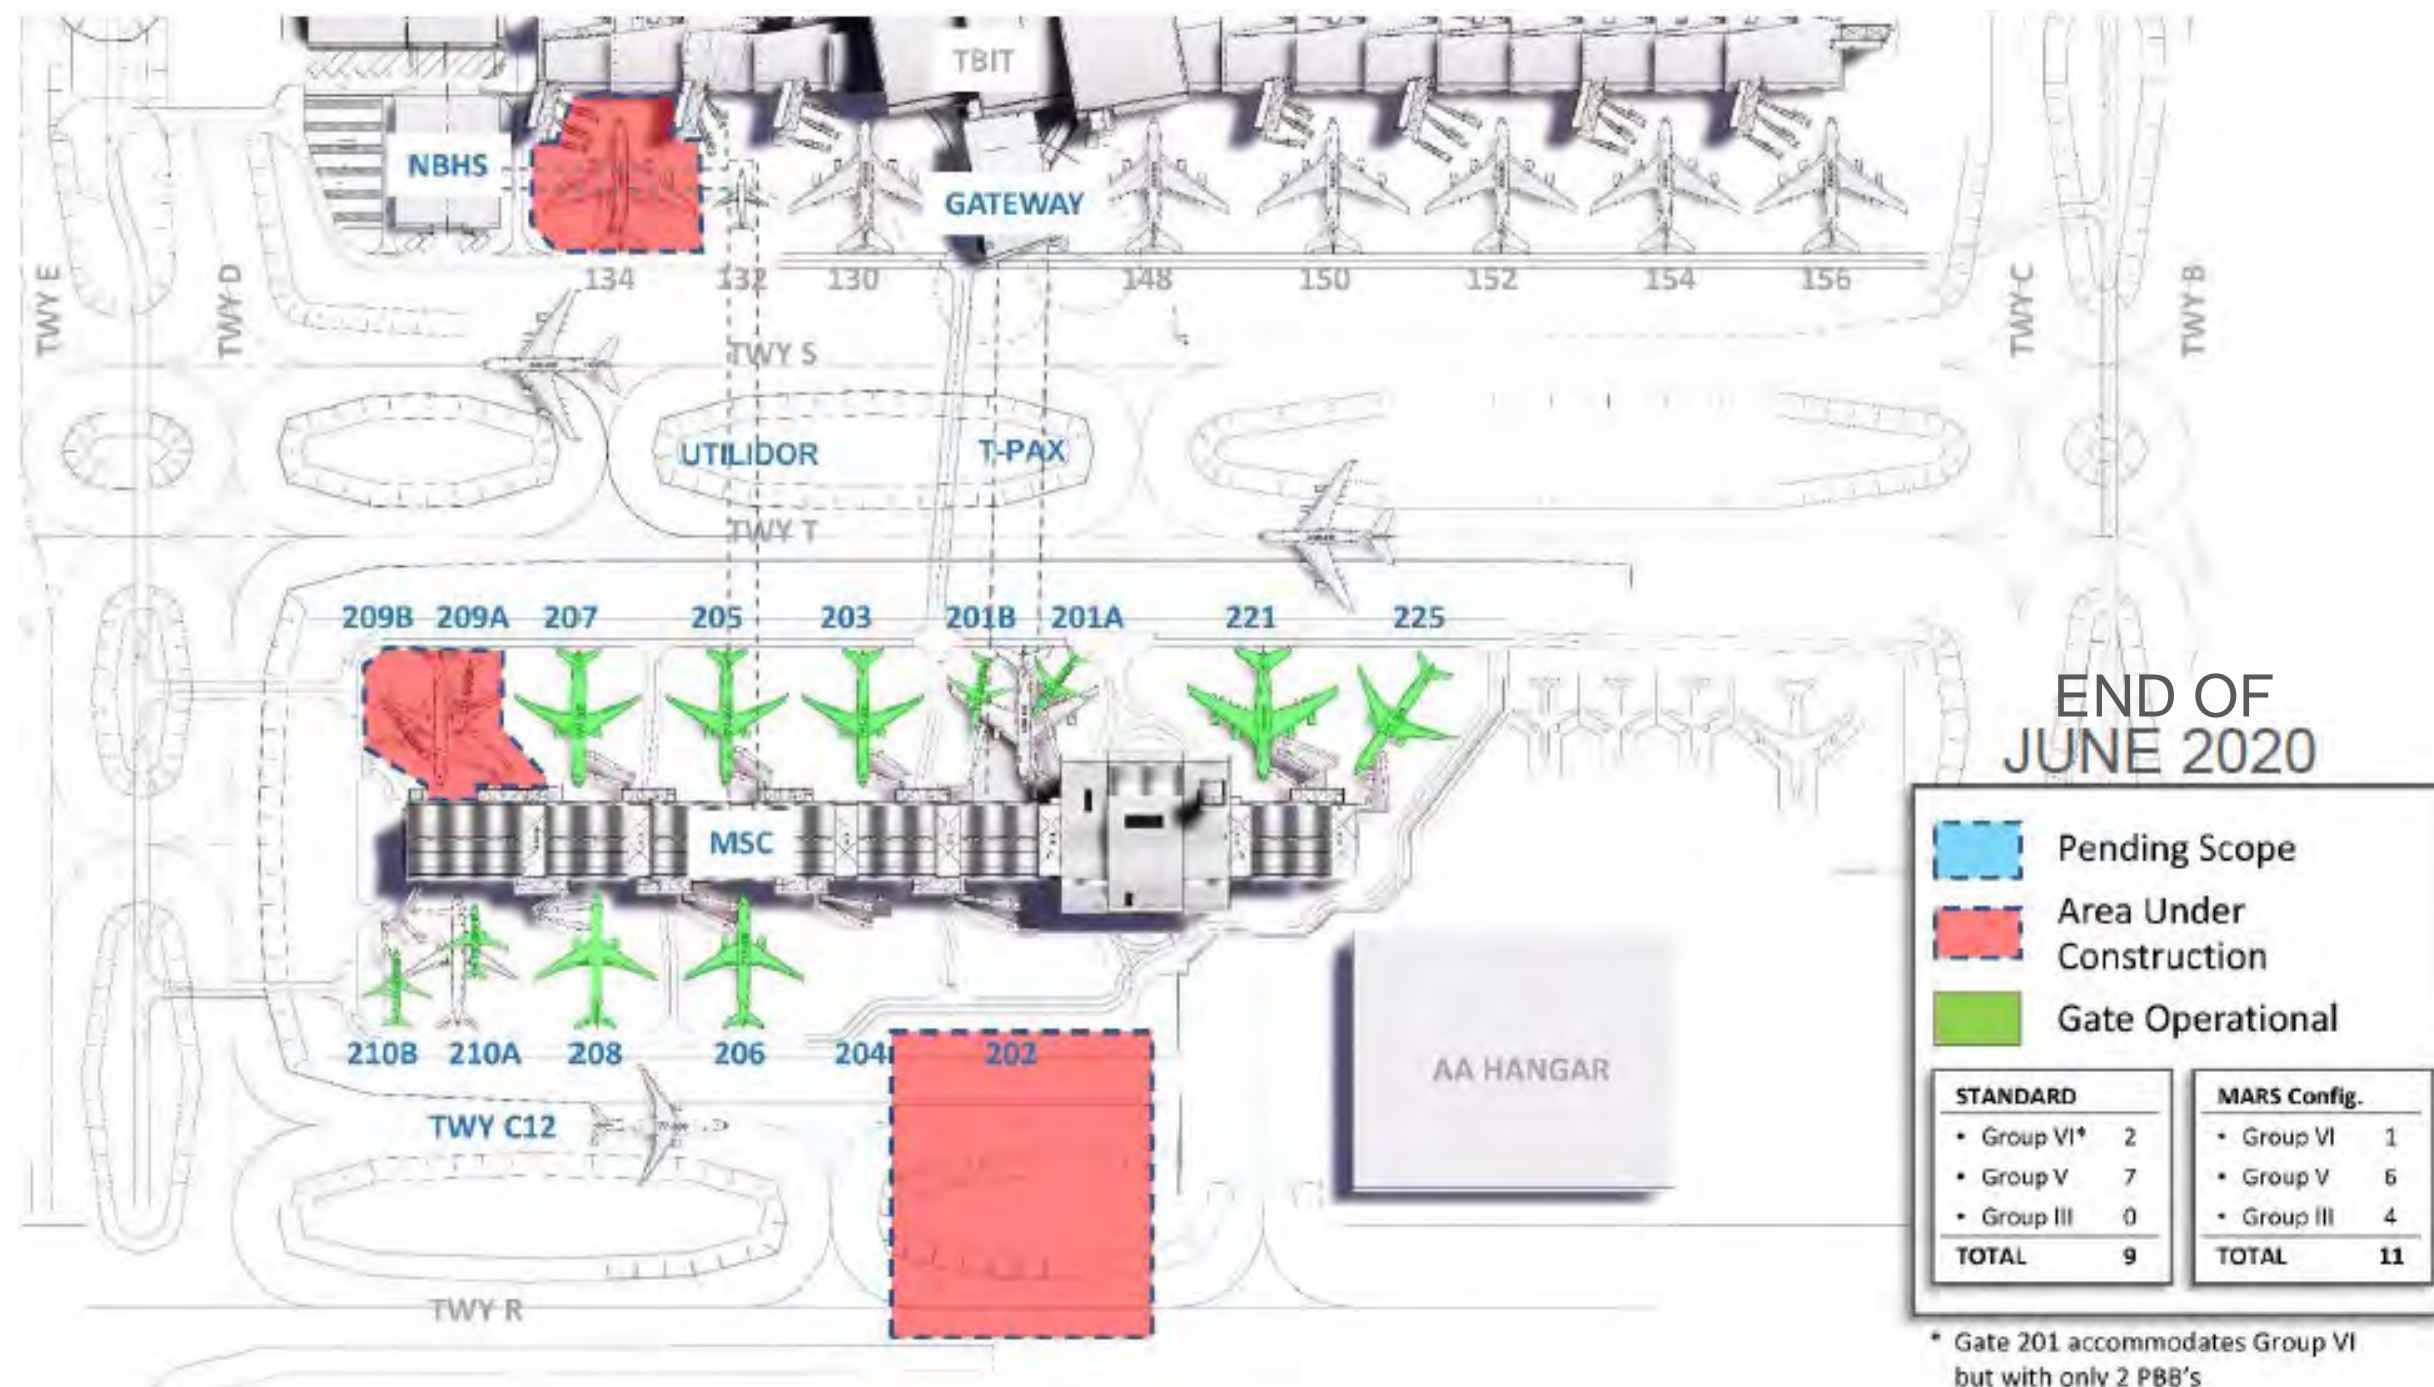


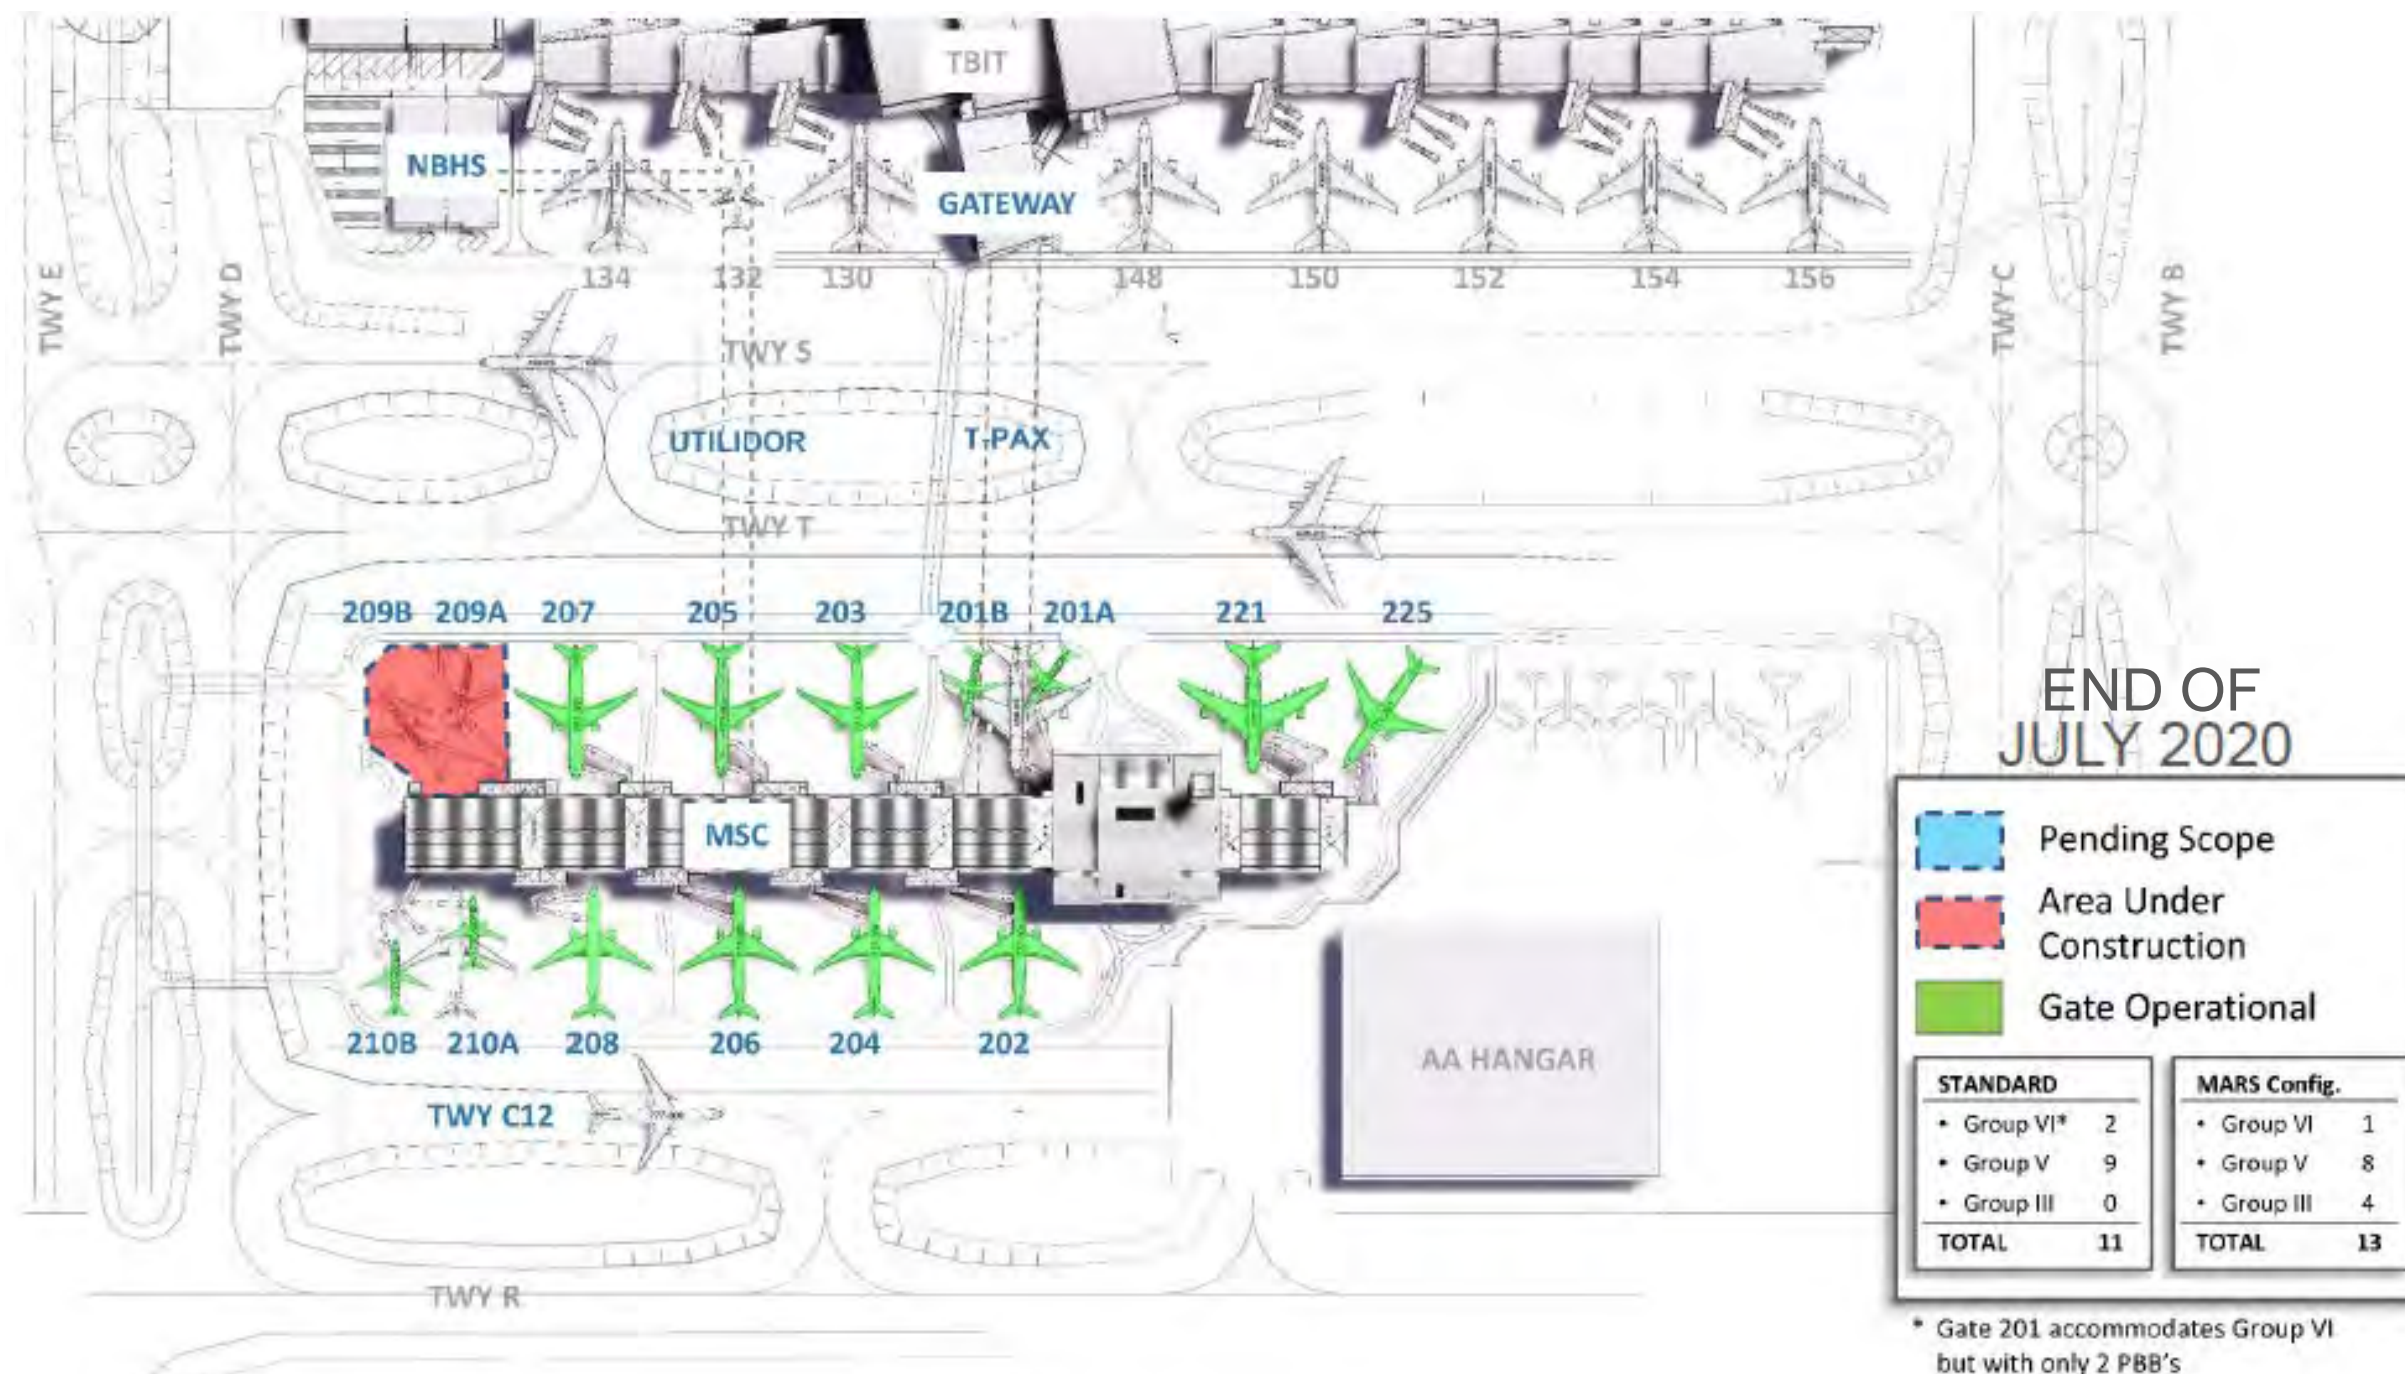

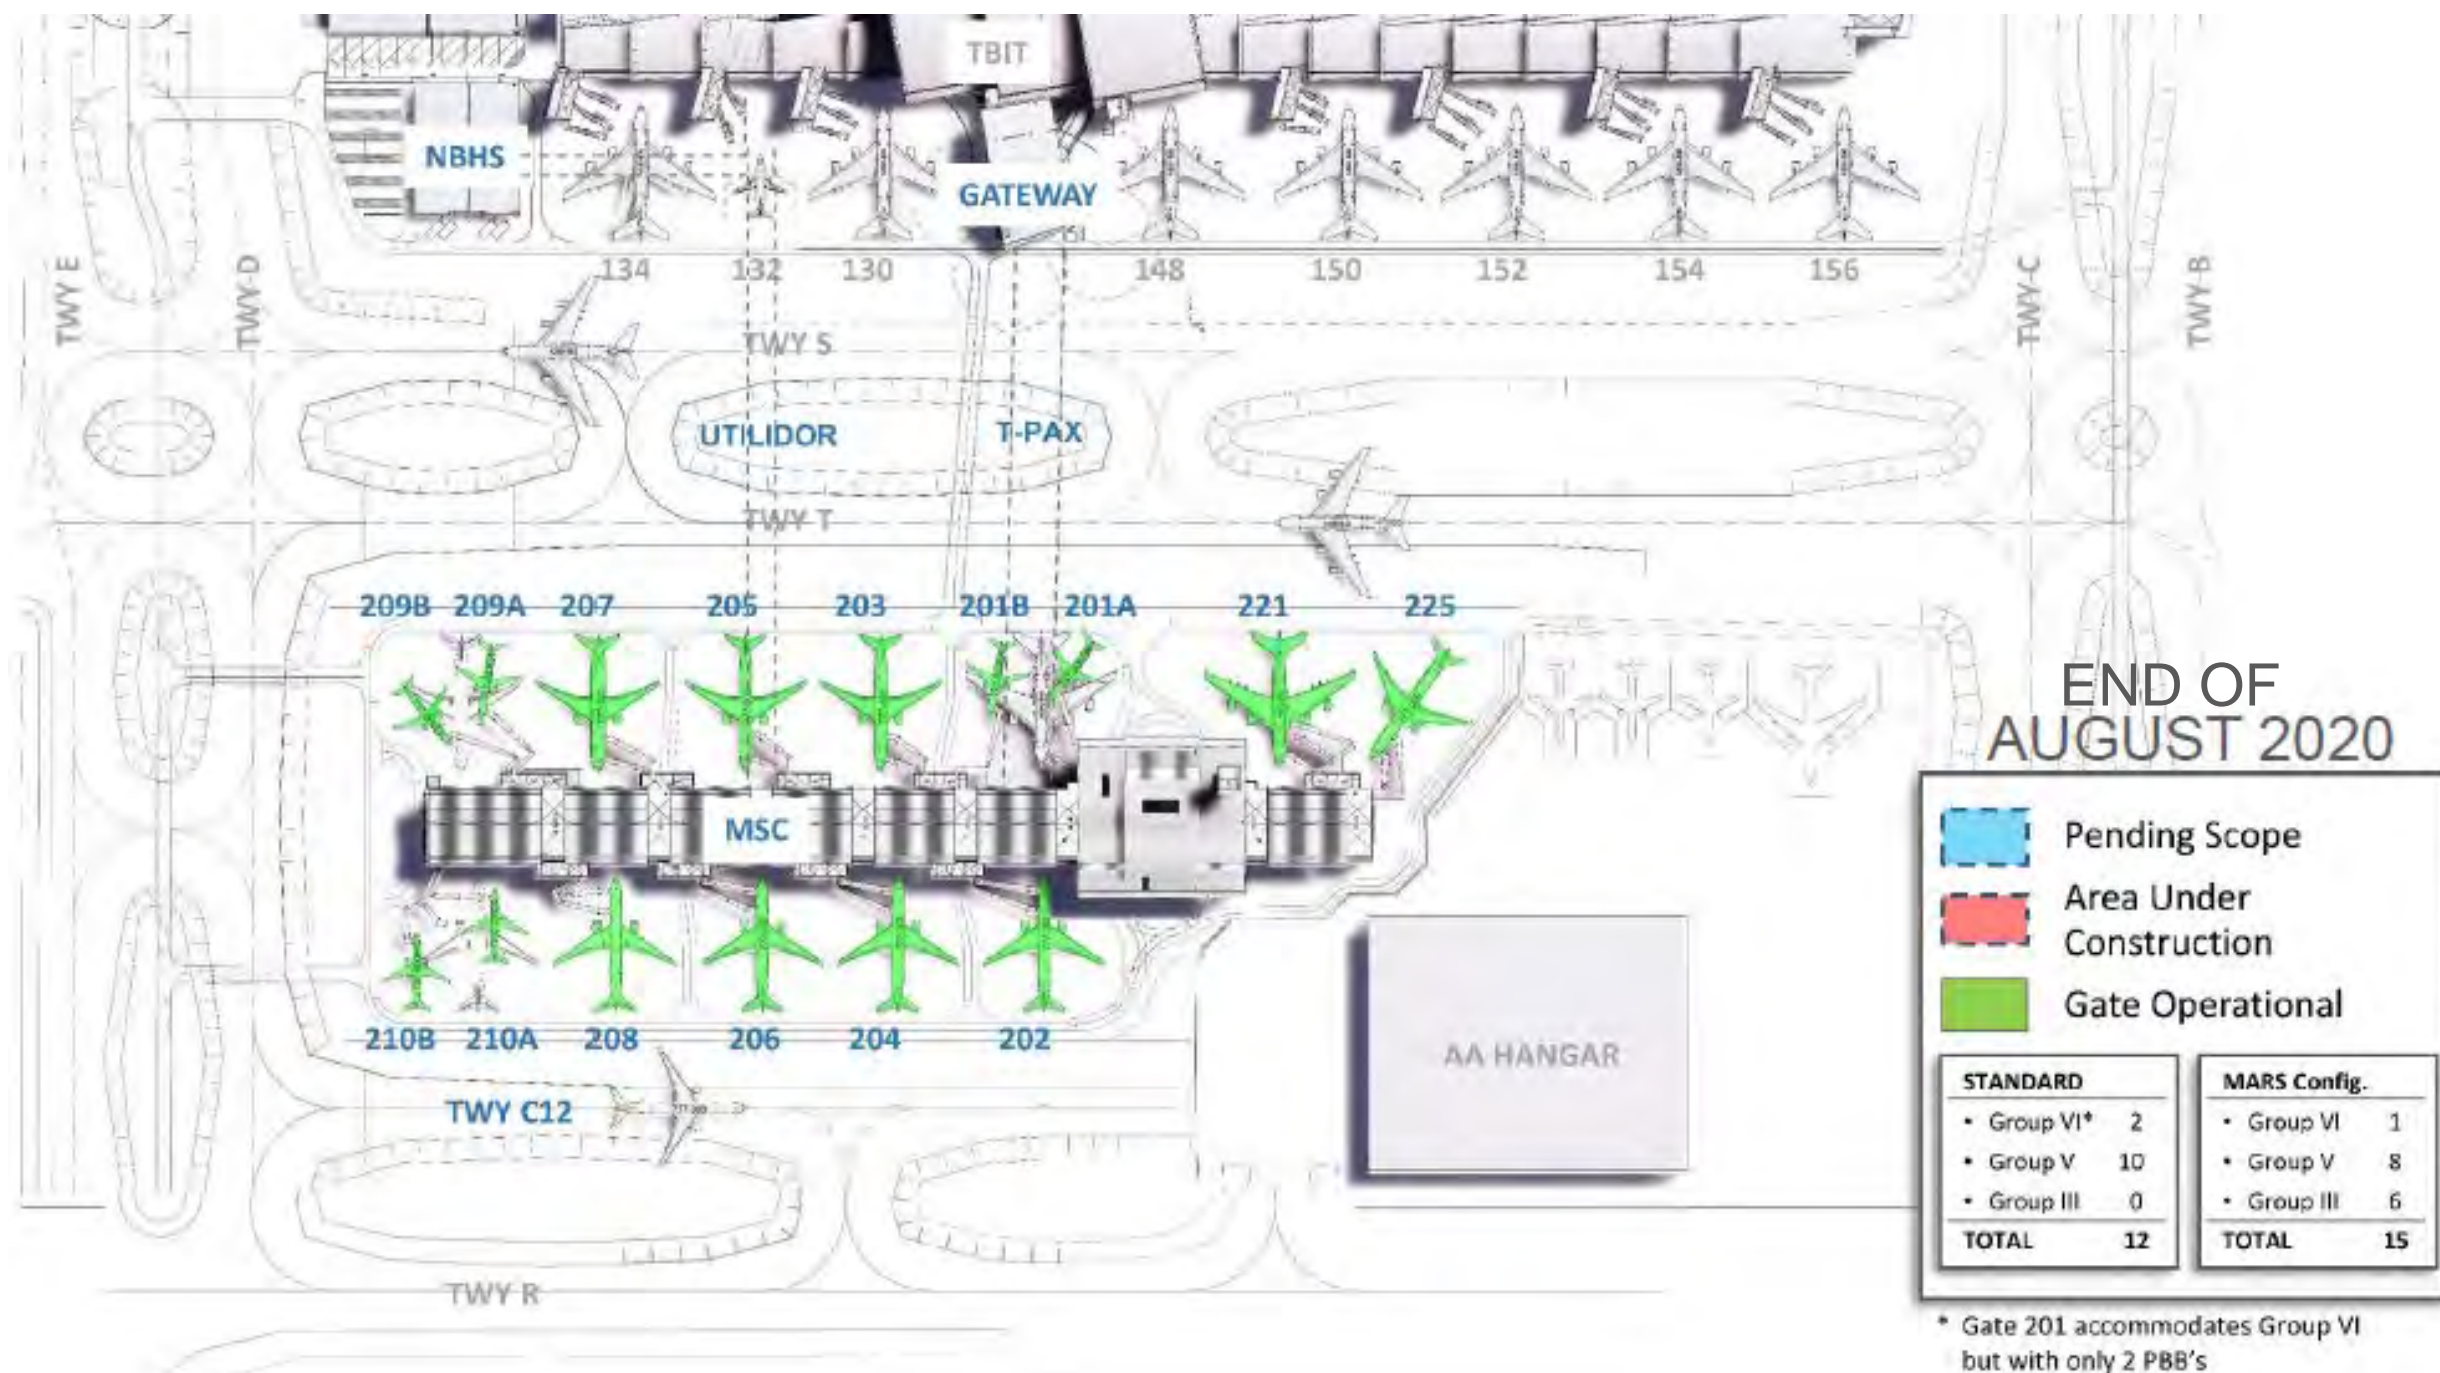

Questions / Feedback





STAKEHOLDER CONSTRUCTION COORDINATION

STAKEHOLDER CONSTRUCTION COORDINATION Number 70	Project # DA-4971
--	--------------------------

Date	Start	Location	Next Meeting	Next Time	Next Location	Prepared By
9/19/2019	09:00 AM	MSC Trailer - Larry Walters Conference Room	10/3/2019	09:00 AM	MSC Trailer - Larry Walters Conference Room	Somvongsiri, Kim

Purpose	General Notes
---------	---------------

Construction Coordination

Attended By	Non-Attendees
-------------	---------------

Arnold, Keith - LAWA Police Department
 Buchanan, Cary - Los Angeles World Airports
 Campbell, Daniel - Los Angeles World Airports
 Chinapen, Sharon - Planning & Development Group
 Cummings, Nick - AvAirPros
 Gilbert, Robert - Los Angeles World Airports
 Gouny, Sam - Planning & Development Group
 Greer, Richard - Planning & Development Group
 Guerrero, Adelina - Planning & Development Group
 Haldeman, John - Los Angeles World Airports
 Hartnett, Larry - Los Angeles World Airports
 Hirsch, Paul - Planning & Development Group
 Huynh, Tung - Transportation Security Administration
 Hyun, Roger - Los Angeles World Airports
 Jones, Steve - Los Angeles World Airports
 Joseph, Vijendra - Los Angeles World Airports
 Kenard, Courtney - Los Angeles World Airports
 Kulachok, Joanne - Planning & Development Group
 Larson, Kelley - TBITEC
 Le, Quy - Planning & Development Group
 Leon Martinez, Noe - Planning & Development Group
 McAdams, Doug - Planning & Development Group
 Molaibaghal, Mohamadhosein - Planning & Development Group
 Mukhlis, Bilal - Los Angeles World Airports
 Nealon, Anthony - Los Angeles World Airports
 Oppel, Robert - Los Angeles World Airports
 Pannunzio, Charles - Los Angeles World Airports
 Patel, Raja - Planning & Development Group
 Rocha, Victor - Los Angeles World Airports
 Sanchez, Michelle - Planning & Development Group
 Seiden, Valentina - U.S. Customs and Border Protection
 Sullivan, Carrie - TBITEC
 Thomspson, Rodney - Los Angeles World Airports
 Tseng, Brandon - Los Angeles World Airports
 Vogt, Kris - Planning & Development Group

Arredondo, David - Los Angeles World Airports
 Ball, Austin - Logplan LLC
 Bentley, Steven - Los Angeles World Airports
 Brown, Jameila - Transportation Security Administration
 Cao, Thomas - Planning & Development Group
 Carpio, Maria - U.S. Customs and Border Protection
 Chico, Victor - Los Angeles World Airports
 Ching, Frank - Planning & Development Group
 Commiato, Dan - Transportation Security Administration
 Crafts, Mike - FAA
 Dorado, Myra - U.S. Customs and Border Protection
 Duenez, Maria - LAWA Police Department
 Eaton, Brandon - Los Angeles World Airports
 Esquivel, Francisco - Los Angeles World Airports
 Figueroa, Marlene - U.S. Customs and Border Protection
 Foley, Sean - LAWA Police Department
 Garcia, Jesus - Los Angeles World Airports
 Gideon, Juan - Los Angeles World Airports
 Gonsalves, Larry - Planning & Development Group
 Gonzalez, Alfred - U.S. Customs and Border Protection
 Groom, Michael - LAWA Airport Ops
 Gruendl, John - Planning & Development Group
 Gutierrez Jr., Jose - U.S. Customs and Border Protection
 Haines, Bob - Los Angeles World Airports
 Hajeid, Joe - FAA
 Harland, Sara - Los Angeles World Airports
 Harris, Jessica - Los Angeles World Airports
 Harris, Shawna - LAWA Police Department
 Herrera, Paul - Los Angeles World Airports
 Hess, Nicholas - Los Angeles World Airports
 Ignacio, Phil - Planning & Development Group
 Ishfaq, Mansoor - Los Angeles World Airports
 Iwamiya, Gregg - Los Angeles World Airports
 Kafaja, Rafah - Planning & Development Group
 Khan, Zafar - Los Angeles World Airports
 Kim, David - Los Angeles World Airports
 Kissoon, Brian - Planning & Development Group
 Lafaurie, Mario - Los Angeles World Airports
 Lam, Hai Au Ho - Los Angeles World Airports
 Lara, Paul - LAWA PD
 Lawrence, Steve - Planning & Development Group

Non-Attendees

Lazarevic, Goran - Los Angeles World Airports
Lee, Kin - FAA
Lee, Laura - U.S. Customs and Border Protection
Lee, Tamra - FAA
Lew, Calvin - Planning & Development Group
Lin, Daniel - Customs Border Protection
Ling, Sandy - AvAirPros
Lomeli, Louis - Transportation Security Administration
Lopez, Mary - Los Angeles World Airports
Luperuo, Jorge - Transportation Security Administration
Ly, Denny - Los Angeles World Airports
Martinez Jr., Luis - Los Angeles World Airports
McElvaney, Michael - Planning & Development Group
McEneaney, Eve - Los Angeles World Airports
McGourty, Kevin - Los Angeles World Airports
McNeil, Heather - U.S. Customs and Border Protection
McNierney, Christopher - American Airlines
Melara, Edward - Los Angeles World Airports
Mendavia, Manilito - LAWA Facility Maintenance Group
Metry, Romany - Los Angeles World Airports
Montoya, Maurice - FAA
Moreno, James - Transportation Security Administration
Mort, Jeff - Los Angeles World Airports
Muchiri, Jackson - LAWA Police Department
Nadler, Baljit - Los Angeles World Airports
Navarrete, Georginnah - Los Angeles World Airports
Nealy, Sean - U.S. Customs and Border Protection
Nguyen, Tom - U.S. Customs and Border Protection
Ojeda, Jimmy - U.S. Customs and Border Protection
Panagiotidis, Paul - Los Angeles World Airports
Patel, Vimal - Los Angeles World Airports
Prasad, Viji - Los Angeles World Airports
Proffitt, Brian - Planning & Development Group
Rasem, Aymen - Planning & Development Group
Roa, Ed - Planning & Development Group
Rodriguez, Victor - Los Angeles World Airports
Rogers, Tim - AvAirPros
Sarullo, Teresa - Los Angeles World Airports
Saucier, Kenneth - Planning & Development Group
Seeram, Ramesh - Los Angeles World Airports
Segura, Jose - LAWA Police Department
Shade, Andrell - Vanderlande
Smets, Laura - Planning & Development Group
Somvongsiri, Kim - Planning & Development Group
Tomcheck, Pat - Los Angeles World Airports
Torrecampo, Vee - Los Angeles World Airports
Tran, Khanh - FAA
Truong, Thanh - FAA
Viramontes, Jose - LAWA Police Department
Wall, Thomas - Planning & Development Group
Waterhouse, Michael - Los Angeles World Airports

Non-Attendees

Williams, Chad - LAWA Airport Ops
 Wirth, Tom - U.S. Customs and Border Protection
 Wong, Gordon - Planning & Development Group
 Woods, Steve - Planning & Development Group
 Yamamoto, Barbara - Los Angeles World Airports
 Zeidan, Majed - Los Angeles World Airports

Courtesy Copy

Item	Description	Responsible	Due Date	Status
No Topic Assigned				

Baggage Handling System (BHS)

023-001 5/31/2018
 A. Eve McEneaney (Terminal Ops) asked that there be discussions on how employees access the temp make-up area.

4/19/2018
 A. Temp make-up area will be turnover to the contractor (VI) on May 1, 2018.

BOP: Far East Tunnel / Gate 131

001-002 4/4/2019
 A. LADWP manhole delivery will not take place on 4/11. It will likely take place the following week.

3/7/2019
 A. Stage 4 VSR field test conducted and adjustments have been made as a result. Including posting flaggers for a week.

11/15/2018
 A. Shift of ACAMS from Door 1801 will impact approx 20 other doors. Coordination with APD under way.

11/1/2018
 A. Area 3 (work on curb outside of vendor roll-down door) expected to be completed in Dec.

10/18/2018
 A. Area 3 facing challenges with vault/manhole connection to ductbank. Possible VSR impact and impact to trash area.

10/4/2018
 A. Ops raised a concern regarding concrete trucks backing into taxilane. And that flaggers are more aware of aircraft pushback.

7/12/2018
 A. Area 3 for DWP vault has a construction duration of approximately 3 months.
 B. The 2 receiving pits on the CTA curb needs to be enlarged. Workplan being developed.

6/14/2018
 A. Eve McEneaney (Terminal Ops) conducted walk with Fire Department who have made requests of the project related to maintaining muster area, etc.
 B. Issues still exists related to Delta Airline jetblast. Cary Buchanan

No Topic Assigned**BOP: Far East Tunnel / Gate 131**

(Ops) has agreed that blacking out 1st stop may be needed.

5/17/2018

A. DWP Power Vaults in the CTA Phase 2 expected to start Jun 4, 2018

4/19/2018

A. MSC team reported jet blast issues from Terminal 3 operations tonto Far East site. Ops will review operations plan with Delta Airlines and will reiterate plan that is in place regarding push-back.

B. CTA vault work will likely start May 14, 2018

BOP: NBHS Structure / IWBT

001-003

5/16/2019

A. Ops has asked the MSC team to remind the lunch truck that it needs to be inside the construction area, not parked outside.

4/4/2019

A. Rodney Thompson (Ops) stated that Delta Airlines needs to be directly involved with bussing operation decisions related to VSR shift.

B. MSC team looking to possibly provide additional staging on west side of IWBT along with staging on north side.

3/21/2019

A. Parapet lights have been installed. The project will leave on the lights to get feedback from Operations & airlines.

11/29/2018

A. Bus Route around south side of NBHS is not expected to shift until Feb 2019.

4/19/2018

A. NBHS steel expected to be completed week of Apr 23, then crane will be removed.

2/8/2018

A. On a test run, steel deliveries into the NBHS site are having difficulty making the turn into the site without impeding Taxiway Sierra. MSC will coordinate with Airport Operations to review access.

DWP Substation

001-004

1/24/2019

A. Closure of R may be necessary to complete DWP work. If needed, MSC team will coordinate with stakeholders.

5/17/2018

A. MSC Team working with CALM to identify parking spots for DWP construction personnel.

4/19/2018

A. Turnover of LADWP substation site to DWP will likely occur 1 week later, on June 22, 2018.

Gateway

001-001

8/8/2019

A. TBITEC (Kelley Larson) asked that a barricade be installed behind

No Topic Assigned**Gateway**

the Bradley doghouse 10A/B for safety reasons. Also, TBITEC requests extra lights to be installed.

1/10/2019

A. Expected dry-in of Gateway in Apr.

11/15/2018

A. Rodney Thompson (Ops) has asked that 10B closure occur after holidays if possible (rather than mid Dec).

10/4/2018

A. Inbound BHS doghouse 10B ASR coordination should include TBITEC due to VI equipment per Eve McEneaney (Terminal Ops).

9/6/2018

A. Gateway Inbound 10A will close temporarily on Oct 1.

8/23/2018

A. Exterior barricade plan at the inbound BHS area is being evaluated for effectiveness.

7/12/2018

A. Interior barricade inside Bradley expected to be in place within next 2 weeks.

6/28/2018

- A. Gateway steel expected to start mid-Jul.
- B. Steel erection over Inbound BHS area will be nightly only.
- C. Electrical outage in the Bradley Core, USR underway.

6/14/2018

A. Eve McEneaney (Terminal Ops) has asked that Gateway Inbound BHS Doghouse 10B Closure does not happen until 3rd week of Sep.

3/22/2018

A. Barricade within Bradley core expected to be installed June 2018 and be in place until Gateway opening.

1/11/2018

A. Courtney Kenard (CDG) asked the Gateway team to coordinate the removal and storage of the VDGS Summary Display with Commercial Development Group (CDG) and Airport Operations.

Miscellaneous

001-007

8/8/2019

A. Ops requires a work plan for all crane activities. This is a new airport requirement and needs to be complied with regarding of prior approval.

4/4/2019

A. Cary Buchanan (Airside Ops) mentioned that there needs to be scope clarification discussion related to Romeo 2 intersection between C14 and MSC teams.

3/21/2019

A. Courtney Kenard (CDG) has asked that any demob/reinstall of PBBs at BW be coordinated with her so that TBITEC/VI can be informed since there are LAWA contractual requirements regarding this item.

No Topic Assigned**Miscellaneous**

2/7/2019

A. Laura Smets (CALM) mentioned Post 236B closure and the need for advance planning for Post 23 traffic.

12/13/2018

A. Ops asked that any work done outside of the identified/approved construction fence line be coordinated in advance with the Construction Desk and Duty Manager.

11/29/2018

A. Static Racks were discussed. AvAirPros will be meeting with Ground Service Providers and Ops to determine if we will proceed with installing at the NBHS and which configuration options.
MSC team needs to know mid-Dec because at that time the current area at Coast Guard Road will need to be vacated.

11/1/2018

A. Power shut-downs at Bradley West will start Mon and continue for 2 weeks. Due to impacts to ACAMs, guards will be in place.

10/4/2018

A. MSC team will be reaching out to CBP regarding possible reduction of airside guards.

8/23/2018

A. CBP has requested guards be in place to watch and ensure that trades people are going directly from bus drop-off locations to respective airside job sites.

5/17/2018

A. Paul Herrera (Ops) mentioned that MSC project will take priority over Delta & T3 Connector work.

2/8/2018

A. Cary Buchanan (Airport Operations) requests exhibits for aircraft movement changes, as a result of the opening of Taxiway T and partial closing of Taxiway S, by the end of February 2018 in order to meet the FAA publication cycle.

MSC

001-005

7/11/2019

A. Taxiway D target date for reopening July 18th, but there may be some panel replacement necessary.

6/13/2019

A. Cary Buchanan (Airside Operations) advised that Ops needs at least 3 days notice for reactivation of Taxiway D.

5/2/2019

A. Cary Buchanan (Airside Operations) asked that the team verify that Taxiway D TOFA for Group VI is met.

3/7/2019

A. Taxiway D expected to be completed in mid-Jun due to recent weather impacts.

No Topic Assigned**MSC**

1/10/2019

A. MSC & C14 projects continue to coordinate. C14 project not yet awarded. MSC drives C14 schedule.

11/29/2018

A. Paving north of MSC as part of the fuel line tie-in project begins mid Dec.

11/15/2018

A. Ramp Control Tower designers for Radio Frequency (Leidos) is on board. Study should be completed by the end of Jan.

10/18/2018

A. Terrazzo mock-up at the north end of the concourse has started.

9/20/2018

A. Ops asked if reflective tape could be added to airfield signs that have been decommissioned for TWY D Fuel Line work.

8/9/2018

A. Sanitary Sewer Pit 4 work expected to begin in Sep.

7/12/2018

A. Upon review of bypass by LADBS, a new procedure is required and being vetted.

B. Fuel Line tie-in impacting TWY D expected to start Sep 17. NOCC to be submitted to APD by Jul 17th.

5/31/2018

A. Cary Buchanan (Ops) stated that TWY 'D' needs to be open and back in service by mid-May 2019.

B. Airport Police noticed some gaps in the fencing on the MSC site. They asked that the MSC team secure the fencing. APD also mentioned that perhaps parking decals would help identify who is authorized to be parked on site. Also, in case of vandalism, employees can call APD to report.

5/3/2018

A. Ops has asked that as pavement gets completed at the north end of MSC, it gets turned over for use.

4/19/2018

A. Cary Buchanan (Ops) prefers that the Fuel Line Tie-in on the north side of the concourse that will impact TWY D to start after Sep 15.

B. MSC team reported that the RON north of Taxiway T would not be available for use after May 14, 2018, Cary Buchanan (Ops) asked the MSC team to prolong use of the RON as long as possible.

3/22/2018

A. MSC crane is scheduled to be back on-site April 9th, 2018. But will likely push back to April 16th, 2018.

1/11/2018

A. Airport Operations stated that the start of Fuel line tie-in work should be done in conjunction with any work needed on the north end of MSC so that Taxiway D closure occurs only once for MSC work.

Non-site specific

No Topic Assigned**Non-site specific**

- 001-006 3/22/2018
 A. Cary Buchanan (Airport Operations) stated that documents are completed for the May 24th, 2018 FAA publication cycle for Taxiway changes.
- 1/25/2018
 A. Cary Buchanan (Airside Operations) reiterated that a 7460 is not approval to do work. 3-day notification is still required.

Tunnels

- 010-001 7/11/2019
 A. Tunnels (Crossover) For Firewater shutdown, water truck will be on stand by in the case it is needed for stand pipes.
- 6/27/19
 A. Tunnels (Crossover) Gate 141, Southwest Airlines Offices sewage spill clean-up and restoration in progress. The flood was due to pump failure.
- 6/13/2019
 A. MSC Team advised the group regarding the AOA security wall at the MSC basement-end of the Passenger Tunnel. This is an ACAM security barricade and not meant for personnel traffic.
- B. Passenger Tunnel to be accessed from airside.
- 5/2/2019
 A. Kelley Larson (TBITEC) asked that the activation of the jetbridges at 132 be coordinated with TBITEC because maintenance work needs to be performed. Steve Lawrence on the MSC team will coordinate.
- 4/18/2019
 A. MSC team will conduct a walk with Maintenance when lift station is installed at 132 area.
- 4/4/2019
 A. MSC reviewing Ops comments regarding aircraft movement for 132 and 134 areas. This includes hold-bars, wing tip clearances, blast fence.
- 3/21/2019
 A. Aircraft push-back at Gate 134 issues. Aircraft wings coming into job site. Ops will meet with GSE providers to address.
 B. Natural Gas shutdown on Mar 29th dependent on Semptra Mar 25th install of new gas meter.
- 2/7/2019
 A. Aircraft Movement for 132 reopening (currently planned for Jul) and closure of 134 with Ops upcoming.
- 11/29/2018
 A. Gate 134 PBBs will remain intact and stowed when Gate 134 Closes.
- 11/15/2018
 A. Nightly impact to Gate 134 for access required. Likely to start end of Dec. Durations TBD.

No Topic Assigned**Tunnels**

9/6/2018

A. MMRP waiver for dirt hauling is in effect through end of Sep.

7/12/2018

A. Passenger Tunnel 12-hour gas shutdown being reviewed and MSC is trying to improve on the duration.

6/28/2018

A. MMRP waver will be submitted for concrete pours at tunnels.

B. Fire Water will be approx 2 month duration. Water will be available but no redundancy.

C. Domestic Water will be nightly shut downs only.

5/31/2018

A. Security wall/door has been activated. The teams should communicate to others that no one is to use these doors. In the case where the alarm is set off, TPJV to collect names of individuals.

3/22/2018

A. MSC team stated that there will be some intermittent impact to Gate 130 and 134. Dates are being coordinated with Airport Operations (Brandon Tseng). Rodney Thompson (Airport Operations) mentioned that Aircraft Service International Group (ASIG) will also be doing fuel work and require shut-downs in mid-April 2018. MSC team and Airport Operations will coordinate.

2/8/2018

A. Utilidor/Crossover hauling expected to end at the end of March 2018.

STAKEHOLDER MEETING SIGN-IN SHEET

Date: Thu - 19 Sep 2019

Location: MSC PMO

Subject: MSC Stakeholder Construction

Organizer: Kim Somvongsiri

Initial	Name (Please print clearly)	Company / Group Affiliation	Phone	Email
1.	Ball, Austin	Logplan	719-233-4472	a.ball@logplan.com
2. <i>CB</i>	Buchanan, Cary	LAWA Ops	424-646-8257	cbuchanan@lawa.org
3. <i>De</i>	Campbell, Dan	LAWA FTSD	424-646-7850	dcampbell2@lawa.org
4.	Carpio, Maria	LAWA CDG	310-568-7501	maria.c.carpio@cbp.dhs.gov
5.	Chico, Victor	LAWA CDG	424-646-7225	vchico@lawa.org
6. <i>Q</i>	Chinapen, Sharon	LAWA AOR	424-646-7505	schinapen@lawa.org
7.	Ching, Frank	LAWA PDG	310-729-3221	fching@lawa.org
8.	Commiato, Dan	DHS/TSA	310-242-9046	dan.commiato@dhs.gov
9. <i>HC</i>	Cummings, Nick	AvAirPros	904-234-0770	n.cummings@avairpros.com
10.	Dorado, Myra	CBP	310-946-6435	myra.a.dorado@cbp.dhs.gov
11.	Eaton, Brandon	LAWA Ops	310-877-0150	beaton@lawa.org
12.	Foley, Sean	LAWA PD	424-646-8227	sfoley@lawa.org
13.	Garcia, Jesus	LAWA Ops	424-646-5292	kgarcia@lawa.org
14.	Gideon, Juan Carlos	LAWA Ops	424-356-9031	kgideon@lawa.org
15.	Gonzalez, Alfred	CBP	310-568-7501	alfred.gonzalez@cbp.dhs.gov
16. <i>AS</i>	Gouny, Sam	LAWA PDG	424-646-5968	sgouny@lawa.org
17. <i>RG</i>	Greer, Richard	LAWA PDG	424-646-8494	rgreer@lawa.org
18. <i>AG</i>	Guerrero, Adelina	LAWA PDG	424-646-9131	aguerrero@lawa.org
19.	Gutierrez, Jose	CBP	949-643-6335	jose.gutierrez-jr@cbp.dhs.gov
20. <i>HB</i>	Haines, Bob	LAWA FTSD	424-646-7849	rhaines@lawa.org
21. <i>JH</i>	Haldeman, John	LAWA AOR	424-646-5887	jhaldeman@lawa.org

STAKEHOLDER MEETING SIGN-IN SHEET

Initial	Name (Please print clearly)	Company / Group Affiliation	Phone	Email
22. 	Hartnett, Larry	LAWA MSD	424-646-7852	lhartnett@lawa.org
23. _____	Herrera, Paul	LAWA Ops	424-646-8250	pherrera@lawa.org
24. 	Hess, Nick	LAWA MSD	424-646-7900	nhess@lawa.org
25. 	Hirsch, Paul	LAWA PDG	443-799-5376	phirsch@lawa.org
26. 	Huynh, Tung	TSA	310-387-1082	tung.huynh@tsa.dhs.gov
27. 	Hyun, Roger	LAWA PDG	424-646-5133	rhyun@lawa.org
28. _____	Ignacio, Phil	LAWA PDG	424-646-7514	pignacio@lawa.org
29. _____	Ishfaq, Mansoor	LAWA AOR	424-646-5193	mishfaq@lawa.org
30. 	Jones, Steve	LAWA AOR	424-646-5242	sjones@lawa.org
31. 	Joseph, Vijendra	LAWA FTSD	424-646-7848	vjoseph@lawa.org
32. _____	Kafaja, Rafa	LAWA AOR	310-648-2002	rkafaja@lawa.org
33. 	Kenard, Courtney	LAWA CDG	424-646-5267	ckenard@lawa.org
34. _____	Khan, Zafar	LAWA CUP	424-646-7828	zkhan@lawa.org
35. _____	Kim, David	LAWA PDG	310-864-9016	dkim@lawa.org
36. _____	Kissoon, Brian	LAWA AOR	424-646-5134	bkissoon@lawa.org
37. 	Kulachok, Joanne	LAWA PDG	424-646-7597	jkulachok@lawa.org
38. _____	Lafaurie, Mario	LAWA Ops	424-646-6681	mlafaurie@lawa.org
39. _____	Lam, Hai	LAWA PDG	924-626-3766	hlam@lawa.org
40. _____	Lara, Paul	LAWA PD	310-491-8035	plara2@lawa.org
41. 	Larson, Kelley	TBITEC	424-239-8612	klarson@tbiteclax.com
42. _____	Lawrence, Steve	LAWA PDG	424-646-8645	slawrence@lawa.org
43. _____	Lazarevic, Goran	LAWA PDG	424-646-5870	glazarevic@lawa.org
44. 	Le, Quy	LAWA PDG	424-646-7027	qle@lawa.org
45. _____	Lee, Laura	CBP	310-625-2183	laura.lee@cbp.dhs.gov

STAKEHOLDER MEETING SIGN-IN SHEET

Initial	Name (Please print clearly)	Company / Group Affiliation	Phone	Email
46. <i>LM</i>	Leon, Noe	LAWA PDG	424-646-5450	nleonmartinez@lawa.org
47. _____	Lin, Daniel	CBP	310-665-4567	daniel.k.lin@cbp.dhs.gov
48. _____	Ling, Sandy	AvAirPros	626-679-2513	s.ling@avairpros.com
49. _____	Martinez, Luis	LAWA CDG	424-646-6165	lmartinezjr@lawa.org
50. <i>DM</i>	McAdams, Doug	LAWA PDG	424-646-7433	dacdams@lawa.org
51. _____	McElvaney, Micheal	LAWA AOR	919-999-6794	mmcelvaney@lawa.org
52. _____	McEneaney, Eve	LAWA Ops	424-646-5029	emceneaney@lawa.org
53. _____	McGourty, Kevin	LAWA MSD	424-646-7029	kmcgourty@lawa.org
54. _____	McNierney, Christopher	American Airlines	310-642-6852	christopher.mcnierney@aa.com
55. _____	Melara, Ed	LAWA MSD	424-646-7900	emelara@lawa.org
56. _____	Mendavia, Manolito	LAWA CUP	310-877-1356	mmendavia@lawa.org
57. _____	Metry, Romany	LAWA PDG	310-809-6090	rmetry@lawa.org
58. <i>MM</i>	Molai, Mo	LAWA PDG	424-646-8619	mmolaibaghal@lawa.org
59. <i>BM</i>	Mukhlis, Bilal	LAWA PDG	714-931-7362	bmukhlis@lawa.org
60. _____	Nadler, Baljit	LAWA CDG	424-646-7218	bnadler@lawa.org
61. <i>Present</i>	Nealon, Tony	LAWA OPS		anealon@lawa.org
62. _____	Nealy, Sean	CBP	949-973-7336	sean.t.nealy@cbp.dhs.gov
63. _____	Nguyen, Tom	CBP	310-665-4567	tom.b.nguyen@cbp.dhs.gov
64. _____	Ojeda, Jimmy	CBP	310-568-7501	jimmy.a.ojeda@cbp.dhs.gov
65. <i>RO</i>	Oppel, Robert	CDG	424-646-7401	roppel@lawa.org
66. _____	Panagiotidis, Paul	LAWA FTSD	424-646-5800	ppanagiotidis@lawa.org
67. <i>JP</i>	Pannunzio, Charles	LAWA PR	424-646-5044	cpannunzio@lawa.org
68. _____	Patel, Jayin	LAWA PDG	310-918-3757	jpatel@lawa.org
69. <i>RP</i>	Patel, Raja	LAWA PDG	310-259-9089	rpatel@lawa.org

STAKEHOLDER MEETING SIGN-IN SHEET

Initial	Name (Please print clearly)	Company / Group Affiliation	Phone	Email
70.	Patel, Vimal	LAWA AOR	424-646-7233	vpatel@lawa.org
71.	Proffit, Brian	LAWA PDG	424-646-7030	bproffit@lawa.org
72.	Rasem, Aymen	LAWA PDG	424-646-7552	arasem@lawa.org
73.	Roa, Ed	LAWA IMTG	424-646-7355	eroa@lawa.org
74. <i>VR</i>	Rocha, Victor	LAWA AOR	310-408-4598	vrocha@lawa.org
75.	Rodriguez, Victor	LAWA MSC	310-887-1447	vrodriquez@lawa.org
76.	Rogers, Tim	AvAirPros	310-997-8030	t.rogers@avairpros.com
77. <i>MS</i>	Sanchez, Michelle	LAWA AOR	909-957-1926	msanchez2@lawa.org
78.	Sarullo, Teresa	LAWA AOR	424-646-5172	tsarullo@lawa.org
79.	Saucier, Kenneth	LAWA PDG	424-646-6752	ksaucier@lawa.org
80.	Seeram, Ramesh	LAWA CUP	310-872-4468	rseeram@lawa.org
81.	Segura, Jose	LAWA PD	310-877-0058	jsegura@lawa.org
82. <i>VLD</i>	Seiden, Val	CBP	562-256-8715	valentina.seiden@cbp.dhs.gov
83.	Shade, Andrell	Vanderlande	310-569-7401	Andrell.Shade@vanderlande.com
84.	Smets, Laura	LAWA CALM	424-646-7157	lsmets@lawa.org
85.	Somvongsiri, Kim	LAWA PDG	424-646-9017	ksomvongsiri@lawa.org
86. <i>CS</i>	Sullivan, Carrie	TBITEC	310-721-7364	csullivan@tbiteclax.com
87. <i>RT</i>	Thompson, Rodney	LAWA Ops	424-646-7480	rthompson@lawa.org
88. <i>BT</i>	Tseng, Brandon	LAWA Ops	310-877-2237	btseng@lawa.org
89. <i>KV</i>	Vogt, Kris	LAWA PDG	424-646-7511	kvogt@lawa.org
90.	Wall, Tom	LAWA SCC	424-646-5368	twall@lawa.org
91.	Waterhouse, Michael	LAWA CDG	424-646-6434	mwaterhouse@lawa.org
92.	Williams, Chad	LAWA Ops	424-646-8282	cwilliams@lawa.org
93.	Wong, Gordon	LAWA PDG	323-243-5207	gwong@lawa.org

STAKEHOLDER MEETING SIGN-IN SHEET

Initial	Name (Please print clearly)	Company / Group Affiliation	Phone	Email
94.	Yamamoto, Barbara	LAWA Guest Experi	424-646-5105	byamamoto@lawa.org
95.	Zeidan, Majed	LAWA PDG	424-646-8116	mzeidan@lawa.org
96.	Alt Andreas Haefner	LAWA AOR	-	ahaefner@lawa.org
97.	KA ARNOLD, KEITH	LAWA APD	424-646-8229	KArnold@lawa.org
98.	Present Gilbert, Bob	LAWA	424-646-5040	bgilbert@lawa.org
99.				
